

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1	UPDATED as of September 1, 2024																			
2	SCE - Local RCI Solicitation	679 days	Tue 8/21/18	Fri 3/26/21																
3	SCE - RFA Preparation	40 days	Tue 8/21/18	Mon 10/15/18																
4	SCE - RFA Release	1 day	Fri 11/9/18	Fri 11/9/18																
5	SCE - RFA Abstract Creation Duration	30 days	Sat 11/10/18	Thu 12/20/18																
6	SCE - RFA Evaluation	82 days	Fri 12/21/18	Mon 4/15/19																
7	SCE - RFA Review with EE PRG	1 day	Tue 4/16/19	Tue 4/16/19																
8	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 5/21/19	Tue 5/21/19																
9	SCE - RFP Preparation	175 days	Wed 5/22/19	Tue 1/21/20																
10	SCE - RFP Release	1 day	Wed 1/22/20	Wed 1/22/20																
11	SCE - RFP Proposal Creation Duration	25 days	Thu 1/23/20	Wed 2/26/20																
12	SCE - RFP Evaluation	38 days	Thu 2/27/20	Mon 4/20/20																
13	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Thu 5/7/20	Thu 5/7/20																
14	SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20																
15	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20																
16	SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20																
17	SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20																
18	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20																
19	SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20																
20	SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21																
21	SCE - SW Lighting	518 days	Wed 4/3/19	Fri 3/26/21																
22	SCE - RFA Preparation	55 days	Wed 4/3/19	Tue 6/18/19																
23	SCE - RFA Release	1 day	Tue 7/2/19	Tue 7/2/19																
24	SCE - RFA Abstract Creation Duration	20 days	Wed 7/3/19	Tue 7/30/19																
25	SCE - RFA Evaluation	34 days	Wed 7/31/19	Mon 9/16/19																
26	SCE - RFA Review with EE PRG	1 day	Tue 9/17/19	Tue 9/17/19																
27	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 9/24/19	Tue 9/24/19																
28	SCE - RFP Preparation	84 days	Wed 9/25/19	Mon 1/20/20																
29	SCE - RFP Release	1 day	Thu 2/6/20	Thu 2/6/20																
30	SCE - RFP Proposal Creation Duration	27 days	Fri 2/7/20	Mon 3/16/20																
31	SCE - RFP Evaluation	25 days	Tue 3/17/20	Mon 4/20/20																
32	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Thu 5/7/20	Thu 5/7/20																
33	SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20																
34	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20																
35	SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20																
36	SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20																
37	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20																
38	SCE - Advice Letter Approved	1 day	Wed 12/23/20	Wed 12/23/20																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
39	SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21																
40	SCE - Local Public Sector Solicitation	573 days	Mon 8/31/20	Wed 11/9/22																
41	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20																
42	SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20																
43	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20																
44	SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21																
45	SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21																
46	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Thu 2/4/21	Thu 2/4/21																
47	SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21																
48	SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21																
49	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21																
50	SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21																
51	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Mon 6/28/21	Mon 6/28/21																
52	SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21																
53	SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21																
54	SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21																
55	SCE - Final Award and Contract Signed	1 day	Tue 12/14/21	Tue 12/14/21																
56	SCE - Submit Advice Letter	37 days	Wed 12/15/21	Thu 2/3/22																
57	SCE - Submit Advice Letter	48 days	Wed 12/15/21	Fri 2/18/22																
58	SCE - Advice Letter Approved	1 day	Thu 8/18/22	Thu 8/18/22																
59	SCE - Implementation Plan	60 days	Thu 8/18/22	Wed 11/9/22																
60	SCE - Local Agriculture Solicitation	512 days	Mon 8/31/20	Tue 8/16/22																
61	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20																
62	SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20																
63	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20																
64	SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21																
65	SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21																
66	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Thu 2/4/21	Thu 2/4/21																
67	SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21																
68	SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21																
69	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21																
70	SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21																
71	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Mon 6/28/21	Mon 6/28/21																
72	SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21																
73	SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21																
74	SCE - Final Award and Contract Signed	1 day	Mon 12/20/21	Mon 12/20/21																
75	SCE - Submit Advice Letter	33 days	Tue 12/21/21	Thu 2/3/22																
76	SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
77	SCE - Final Award and Contract Signed	1 day	Wed 12/15/21	Wed 12/15/21																
78	SCE - Submit Advice Letter	56 days	Thu 12/16/21	Thu 3/3/22																
79	SCE - Advice Letter Approved	1 day	Fri 4/22/22	Fri 4/22/22																
80	SCE - Implementation Plan	60 days	Sat 4/23/22	Thu 7/14/22																
81	SCE - SW Water/Wastewater Solicitation	522 days	Mon 11/16/20	Tue 11/15/22																
82	SCE - RFA Preparation	70 days	Mon 11/16/20	Fri 2/19/21																
83	SCE - RFA Release	1 day	Thu 3/4/21	Thu 3/4/21																
84	SCE - RFA Abstract Creation Duration	29 days	Thu 3/4/21	Tue 4/13/21																
85	SCE - RFA Evaluation	20 days	Wed 4/14/21	Tue 5/11/21																
86	SCE - RFA Review with EE PRG	1 day	Tue 5/18/21	Tue 5/18/21																
87	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Thu 5/27/21	Thu 5/27/21																
88	SCE - RFP Preparation	34 days	Mon 4/19/21	Thu 6/3/21																
89	SCE - RFP Release	1 day	Thu 7/1/21	Thu 7/1/21																
90	SCE - RFP Proposal Creation Duration	25 days	Fri 7/2/21	Thu 8/5/21																
91	SCE - RFP Evaluation	41 days	Fri 8/6/21	Fri 10/1/21																
92	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 10/26/21	Tue 10/26/21																
93	SCE - RFP Review with EE PRG	1 day	Tue 10/19/21	Tue 10/19/21																
94	SCE - Contract Negotiation and Development	94 days	Wed 10/27/21	Mon 3/7/22																
95	SCE - Contract Review with EE PRG	1 day	Tue 3/15/22	Tue 3/15/22																
96	SCE - Final Award and Contract Signed	1 day	Tue 4/19/22	Tue 4/19/22																
97	SCE - Submit Advice Letter	40 days	Wed 4/20/22	Tue 6/14/22																
98	SCE - Advice Letter Approved	26 days	Wed 6/15/22	Wed 7/20/22																
99	SCE - Implementation Plan	44 days	Thu 7/21/22	Tue 9/20/22																
100	SCE - SW ETP Solicitation	466 days	Fri 5/1/20	Fri 2/11/22																
101	SCE - RFA Preparation	57 days	Fri 5/1/20	Mon 7/20/20																
102	SCE - RFA Release	1 day	Tue 8/4/20	Tue 8/4/20																
103	SCE - RFA Abstract Creation Duration	24 days	Fri 8/7/20	Wed 9/9/20																
104	SCE - RFA Evaluation	16 days	Thu 9/10/20	Thu 10/1/20																
105	SCE - RFA Review with EE PRG	1 day	Tue 10/20/20	Tue 10/20/20																
106	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 10/27/20	Tue 10/27/20																
107	SCE - RFP Preparation	42 days	Tue 9/8/20	Wed 11/4/20																
108	SCE - RFP Release	1 day	Tue 1/5/21	Tue 1/5/21																
109	SCE - RFP Proposal Creation Duration	37 days	Tue 1/5/21	Wed 2/24/21																
110	SCE - RFP Evaluation	28 days	Wed 2/24/21	Fri 4/2/21																
111	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 4/27/21	Tue 4/27/21																
112	SCE - RFP Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21																
113	SCE - Contract Negotiation and Development	69 days	Wed 4/21/21	Mon 7/26/21																
114	SCE - Contract Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
115	SCE - Final Award and Contract Signed	1 day	Tue 9/14/21	Tue 9/14/21																
116	SCE - Submit Advice Letter	18 days	Wed 9/15/21	Fri 10/8/21																
117	SCE - Advice Letter Approved	1 day	Tue 11/9/21	Tue 11/9/21																
118	SCE - Implementation Plan	60 days	Wed 11/10/21	Tue 2/1/22																
119	SCE - SW Higher-Education Solicitation	547 days?	Thu 10/1/20	Fri 11/4/22																
120	SCE - RFA Preparation	89 days	Thu 10/1/20	Tue 2/2/21																
121	SCE - RFA Release	1 day	Thu 2/4/21	Thu 2/4/21																
122	SCE - RFA Abstract Creation Duration	19 days	Fri 2/5/21	Wed 3/3/21																
123	SCE - RFA Evaluation	31 days	Thu 3/4/21	Thu 4/15/21																
124	SCE - RFA Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21																
125	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Thu 4/29/21	Thu 4/29/21																
126	SCE - RFP Preparation	39 days	Mon 3/22/21	Thu 5/13/21																
127	SCE - RFP Release	1 day	Fri 5/28/21	Fri 5/28/21																
128	SCE - RFP Proposal Creation Duration	24 days	Fri 6/4/21	Wed 7/7/21																
129	SCE - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21																
130	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Mon 8/30/21	Mon 8/30/21																
131	SCE - RFP Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21																
132	SCE - Contract Negotiation and Development	95 days	Fri 9/3/21	Thu 1/13/22																
133	SCE - Contract Review with EE PRG	1 day	Tue 1/18/22	Tue 1/18/22																
134	SCE - Final Award and Contract Signed	1 day	Sun 3/6/22	Sun 3/6/22																
135	SCE - Submit Advice Letter	1 day	Tue 4/19/22	Tue 4/19/22																
136	SCE - Advice Letter Approved	1 day	Mon 8/15/22	Mon 8/15/22																
137	SCE - Implementation Plan	60 days	Mon 8/15/22	Fri 11/4/22																
138	SCE - Local Equity Residential and SMB	384 days?	Tue 2/15/22	Fri 8/4/23																
139	SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22																
140	SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22																
141	SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22																
142	SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22																
143	SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22																
144	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 6/7/22	Tue 6/7/22																
145	SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22																
146	SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22																
147	SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22																
148	SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22																
149	SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22																
150	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22																
151	SCE - Contract Negotiation and Development	65 days	Wed 11/2/22	Tue 1/31/23																
152	SCE - Contract Review with EE PRG	1 day	Tue 2/21/23	Tue 2/21/23																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
153	SCE - Final Award and Contract Signed	1 day	Thu 3/30/23	Thu 3/30/23																
154	SCE - Submit Advice Letter	22 days	Sun 4/3/22	Mon 5/2/22																
155	SCE - Advice Letter Approved	28 days	Tue 5/2/23	Thu 6/8/23																
156	SCE - Implementation Plan	45 days	Thu 6/8/23	Wed 8/9/23																
157																				
158	SCE - Local Equity SMB	431 days?	Tue 2/15/22	Tue 10/10/23																
159	SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22																
160	SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22																
161	SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22																
162	SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22																
163	SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22																
164	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidd	1 day	Tue 6/7/22	Tue 6/7/22																
165	SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22																
166	SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22																
167	SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22																
168	SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22																
169	SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22																
170	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22																
171	SCE - Contract Negotiation and Development	108 days	Wed 11/2/22	Fri 3/31/23																
172	SCE - Contract Review with EE PRG	1 day	Tue 4/18/23	Tue 4/18/23																
173	SCE - Final Award and Contract Signed	1 day	Wed 5/31/23	Wed 5/31/23																
174	SCE - Submit Advice Letter	22 days	Mon 6/6/22	Tue 7/5/22																
175	SCE - Advice Letter Approved	24 days	Thu 7/6/23	Tue 8/8/23																
176	SCE - Implementation Plan	45 days	Wed 8/9/23	Tue 10/10/23																
177	SCE - Local Strategic Energy Management Solicitation	372 days?	Thu 12/1/22	Fri 5/3/24																
178	SCE - RFP Preparation	85 days	Thu 12/1/22	Wed 3/29/23																
179	SCE - RFP Release	1 day	Fri 4/7/23	Fri 4/7/23																
180	SCE - RFP Proposal Creation Duration	35 days	Fri 4/7/23	Thu 5/25/23																
181	SCE - RFP Evaluation	22 days	Thu 6/1/23	Fri 6/30/23																
182	SCE - RFP Review with EE PRG	1 day	Tue 7/18/23	Tue 7/18/23																
183	SCE - Contract Negotiation and Development	86 days	Tue 8/1/23	Tue 11/28/23																
184	SCE - Contract Review with EE PRG	1 day	Tue 12/19/23	Tue 12/19/23																
185	SCE - Final Award and Contract Signed	6 days	Fri 1/19/24	Fri 1/26/24																
186	SCE - Submit Advice Letter	34 days	Wed 1/31/24	Mon 3/18/24																
187	SCE - Advice Letter Approved	40 days	Tue 3/19/24	Mon 5/13/24																
188	SCE - Local Large Commercial Solicitation	488 days?	Mon 6/26/23	Wed 5/7/25																
189	SCE - RFP Preparation	35 days	Mon 6/26/23	Fri 8/11/23																
190	SCE - RFP Release	1 day	Thu 8/17/23	Thu 8/17/23																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2		
191	SCE - RFP Proposal Creation Duration	41 days	Thu 8/17/23	Thu 10/12/23																
192	SCE - RFP Paused	1 day	Fri 10/13/23	Fri 10/13/23																
193	SCE - Residential Multifamily	326 days?	Fri 9/1/23	Fri 11/29/24																
194	SCE - RFP Preparation	47 days	Fri 9/1/23	Mon 11/6/23																
195	SCE - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23																
196	SCE - RFP Proposal Creation Duration	48 days	Mon 11/6/23	Wed 1/10/24																
197	SCE - RFP Evaluation	25 days	Thu 1/11/24	Wed 2/14/24																
198	SCE - RFP Review with EE PRG	1 day	Tue 2/20/24	Tue 2/20/24																
199	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidd	1 day	Wed 2/28/24	Wed 2/28/24																
200	SCE - Contract Negotiation and Development	70 days	Mon 3/4/24	Fri 6/7/24																
201	SCE - Contract Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24																
202	SCE - Final Award and Contract Signed	15 days	Mon 7/29/24	Fri 8/16/24																
203	SCE - Submit Advice Letter	31 days	Mon 8/19/24	Mon 9/30/24																
204	SCE - Advice Letter Approved	1 day	Fri 11/29/24	Fri 11/29/24																
205	SCE - Local Large Industrial	293 days?	Fri 11/3/23	Tue 12/17/24																
206	SCE - RFP Preparation	17 days	Fri 11/3/23	Mon 11/27/23																
207	SCE - RFP Release	1 day	Mon 12/11/23	Mon 12/11/23																
208	SCE - RFP Proposal Creation Duration	49 days	Mon 12/11/23	Thu 2/15/24																
209	SCE - RFP Evaluation	35 days	Fri 2/16/24	Thu 4/4/24																
210	SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24																
211	SCE - RFP Estimated Notification of Successful and Unsuccessful Bi	1 day	Tue 4/23/24	Tue 4/23/24																
212	SCE - Contract Negotiation and Development	73 days	Wed 4/24/24	Fri 8/2/24																
213	SCE - Contract Review with EE PRG	1 day	Tue 9/17/24	Tue 9/17/24																
214	SCE - Final Award and Contract Signed	10 days	Wed 10/2/24	Tue 10/15/24																
215	SCE - Submit Advice Letter	23 days	Wed 10/16/24	Fri 11/15/24																
216	SCE - Advice Letter Approved	22 days	Mon 11/18/24	Tue 12/17/24																
217	SCE - MAP - All Sectors	299 days?	Mon 11/20/23	Thu 1/9/25																
218	SCE - RFP Preparation	20 days	Mon 11/20/23	Fri 12/15/23																
219	SCE - RFP Release	1 day	Mon 1/8/24	Mon 1/8/24																
220	SCE - RFP Proposal Creation Duration	40 days	Mon 1/8/24	Fri 3/1/24																
221	SCE - RFP Evaluation	30 days	Mon 3/4/24	Fri 4/12/24																
222	SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24																
223	SCE - RFP Estimated Notification of Successful and Unsuccessful Bi	1 day	Wed 4/24/24	Wed 4/24/24																
224	SCE - Contract Negotiation and Development	108 days	Wed 5/1/24	Fri 9/27/24																
225	SCE - Contract Review with EE PRG	1 day	Tue 10/15/24	Tue 10/15/24																
226	SCE - Final Award and Contract Signed	11 days	Tue 10/29/24	Tue 11/12/24																
227	SCE - Submit Advice Letter	35 days	Wed 11/13/24	Tue 12/31/24																
228	SCE - Advice Letter Approved	30 days	Fri 1/31/25	Thu 3/13/25																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2		
229	SCE - Residential	360 days?	Mon 11/20/23	Fri 4/4/25																
230	SCE - RFP Preparation	20 days	Tue 1/16/24	Mon 2/12/24																
231	SCE - RFP Release	1 day	Thu 3/28/24	Thu 3/28/24																
232	SCE - RFP Proposal Creation Duration	41 days	Thu 3/28/24	Thu 5/23/24																
233	SCE - RFP Evaluation	35 days	Fri 5/24/24	Thu 7/11/24																
234	SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24																
235	SCE - RFP Estimated Notification of Successful and Unsuccessful Bi	1 day	Mon 8/5/24	Mon 8/5/24																
236	SCE - Contract Negotiation and Development	80 days	Mon 8/19/24	Fri 12/6/24																
237	SCE - Contract Review with EE PRG	1 day	Tue 12/17/24	Tue 12/17/24																
238	SCE - Final Award and Contract Signed	11 days	Mon 1/13/25	Mon 1/27/25																
239	SCE - Submit Advice Letter	23 days	Mon 2/3/25	Wed 3/5/25																
240	SCE - Advice Letter Approved	22 days	Thu 3/6/25	Fri 4/4/25																
241																				
242	SCE - Local Comprehensive Commercial Solicitation	388 days?	Mon 11/13/23	Wed 5/7/25																
243	SCE - RFP Preparation	73 days	Mon 11/13/23	Wed 2/21/24																
244	SCE - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24																
245	SCE - RFP Proposal Creation Duration	43 days	Thu 2/29/24	Mon 4/29/24																
246	SCE - RFP Evaluation	54 days	Tue 4/30/24	Fri 7/12/24																
247	SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24																
248	SCE - RFP Estimated Notification of Successful and Unsuccessful	1 day	Mon 7/29/24	Mon 7/29/24																
249	SCE - Contract Negotiation and Development	89 days	Tue 7/30/24	Fri 11/29/24																
250	SCE - Contract Review with EE PRG	1 day	Tue 1/21/25	Tue 1/21/25																
251	SCE - Final Award and Contract Signed	1 day	Wed 3/5/25	Wed 3/5/25																
252	SCE - Submit Advice Letter	25 days	Thu 4/3/25	Wed 5/7/25																
253	SCE - Advice Letter Approved	1 day	Wed 5/7/25	Wed 5/7/25																
254																				
255	SCG - Local Single Family Solicitation	660 days	Sun 7/1/18	Thu 1/7/21																
256	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18																
257	SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18																
258	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19																
259	SCG - RFA Evaluation	39 days	Mon 1/7/19	Thu 2/28/19																
260	SCG - RFA Review with EE PRG	1 day	Tue 3/5/19	Tue 3/5/19																
261	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Mon 6/3/19	Mon 6/3/19																
262	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19																
263	SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19																
264	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19																
265	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19																
266	SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
267	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 1/21/20	Tue 1/21/20																
268	SCG - Contract Negotiation and Development	69 days	Mon 1/27/20	Thu 4/30/20																
269	SCG - Contract Review with EE PRG	14 days	Tue 5/5/20	Fri 5/22/20																
270	SCG - Final Award and Contract Signed	8 days	Mon 5/25/20	Wed 6/3/20																
271	SCG - Submit Advice Letter	96 days	Mon 6/1/20	Mon 10/12/20																
272	SCG - Advice Letter Approved	1 day	Thu 11/12/20	Thu 11/12/20																
273	SCG - Implementation Plan	41 days	Fri 11/13/20	Fri 1/8/21																
274	SCG - Local Multi-family Solicitation	735 days	Sun 7/1/18	Thu 4/22/21																
275	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18																
276	SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18																
277	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19																
278	SCG - RFA Evaluation	59 days	Mon 1/7/19	Thu 3/28/19																
279	SCG - RFA Review with EE PRG	1 day	Tue 4/2/19	Tue 4/2/19																
280	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Mon 6/3/19	Mon 6/3/19																
281	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19																
282	SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19																
283	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19																
284	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19																
285	SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19																
286	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 1/21/20	Tue 1/21/20																
287	SCG - Contract Negotiation and Development	155 days	Mon 1/27/20	Fri 8/28/20																
288	SCG - Contract Review with EE PRG	99 days	Tue 5/5/20	Fri 9/18/20																
289	SCG - Final Award and Contract Signed	8 days	Mon 9/21/20	Wed 9/30/20																
290	SCG - Submit Advice Letter	37 days	Thu 10/1/20	Fri 11/20/20																
291	SCG - Advice Letter Approved	1 day	Sun 5/2/21	Sun 5/2/21																
292	SCG - Implementation Plan	51 days	Mon 5/3/21	Mon 7/12/21																
293	SCG - Local Small/Medium Commercial Solicitation	641 days	Tue 9/4/18	Tue 2/16/21																
294	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19																
295	SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19																
296	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19																
297	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19																
298	SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19																
299	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Thu 8/1/19	Thu 8/1/19																
300	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19																
301	SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19																
302	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19																
303	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19																
304	SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
305	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 1/21/20	Tue 1/21/20																
306	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20																
307	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20																
308	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20																
309	SCG - Submit Advice Letter	59 days	Tue 9/1/20	Fri 11/20/20																
310	SCG - Advice Letter Approved	1 day	Fri 12/18/20	Fri 12/18/20																
311	SCG - Implementation Plan	43 days	Sat 12/19/20	Tue 2/16/21																
312	SCG - Local Small/Medium Public Solicitation	631 days	Tue 9/4/18	Tue 2/2/21																
313	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19																
314	SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19																
315	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19																
316	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19																
317	SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19																
318	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Thu 8/1/19	Thu 8/1/19																
319	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19																
320	SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19																
321	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19																
322	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19																
323	SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19																
324	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 1/21/20	Tue 1/21/20																
325	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20																
326	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20																
327	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20																
328	SCG - Submit Advice Letter	49 days	Tue 9/1/20	Fri 11/6/20																
329	SCG - Advice Letter Approved	1 day	Fri 12/4/20	Fri 12/4/20																
330	SCG - Implementation Plan	43 days	Sat 12/5/20	Tue 2/2/21																
331	SCG - Statewide POS Food Service Solicitation	605 days	Mon 1/21/19	Fri 5/14/21																
332	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19																
333	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19																
334	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19																
335	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19																
336	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19																
337	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	0 days	Fri 1/24/20	Fri 1/24/20																
338	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19																
339	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20																
340	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20																
341	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20																
342	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
343	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	0 days	Fri 5/15/20	Fri 5/15/20																
344	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20																
345	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20																
346	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20																
347	SCG - Submit Advice Letter	32 days	Mon 11/2/20	Tue 12/15/20																
348	SCG - Advice Letter Approved	1 day	Thu 1/14/21	Thu 1/14/21																
349	SCG - Implementation Plan	42 days	Fri 1/15/21	Mon 3/15/21																
350	SCG - Statewide Midstream Water Heating Solicitation	597 days	Mon 1/21/19	Tue 5/4/21																
351	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19																
352	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19																
353	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19																
354	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19																
355	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19																
356	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	0 days	Fri 1/24/20	Fri 1/24/20																
357	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19																
358	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20																
359	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20																
360	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20																
361	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20																
362	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	0 days	Fri 5/15/20	Fri 5/15/20																
363	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20																
364	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20																
365	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20																
366	SCG - Submit Advice Letter	25 days	Mon 11/2/20	Fri 12/4/20																
367	SCG - Advice Letter Approved	1 day	Thu 3/18/21	Thu 3/18/21																
368	SCG - Implementation Plan	22 days	Fri 3/19/21	Mon 4/19/21																
369	SCG - Statewide Gas Emerging Technology Solicitation	738 days	Wed 1/2/19	Fri 10/29/21																
370	SCG - RFA Preparation	283 days	Wed 1/2/19	Fri 1/31/20																
371	SCG - RFA Release	1 day	Wed 2/12/20	Wed 2/12/20																
372	SCG - RFA Abstract Creation Duration	30 days	Thu 2/13/20	Wed 3/25/20																
373	SCG - RFA Evaluation	26 days	Thu 3/26/20	Thu 4/30/20																
374	SCG - RFA Review with EE PRG	1 day	Tue 5/5/20	Tue 5/5/20																
375	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Fri 5/15/20	Fri 5/15/20																
376	SCG - RFP Preparation	66 days	Fri 5/1/20	Fri 7/31/20																
377	SCG - RFP Release	1 day	Fri 8/21/20	Fri 8/21/20																
378	SCG - RFP Proposal Creation Duration	30 days	Mon 8/24/20	Fri 10/2/20																
379	SCG - RFP Evaluation	38 days	Mon 10/5/20	Wed 11/25/20																
380	SCG - RFP Review with EE PRG	1 day	Tue 12/1/20	Tue 12/1/20																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
381	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Mon 12/7/20	Mon 12/7/20																
382	SCG - Contract Negotiation and Development	85 days	Mon 1/4/21	Fri 4/30/21																
383	SCG - Contract Review with EE PRG	9 days	Tue 5/4/21	Fri 5/14/21																
384	SCG - Final Award and Contract Signed	29 days	Mon 5/17/21	Thu 6/24/21																
385	SCG - Submit Advice Letter	23 days	Sun 6/27/21	Tue 7/27/21																
386	SCG - Advice Letter Approved	1 day	Tue 8/24/21	Tue 8/24/21																
387	SCG - Implementation Plan	44 days	Wed 8/25/21	Sat 10/23/21																
388	SCG - Local Manufactured Housing Solicitation	341 days	Fri 11/1/19	Fri 2/19/21																
389	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20																
390	SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20																
391	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20																
392	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20																
393	SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20																
394	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	0 days	Mon 6/8/20	Mon 6/8/20																
395	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20																
396	SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20																
397	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20																
398	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20																
399	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20																
400	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 10/13/20	Tue 10/13/20																
401	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20																
402	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20																
403	SCG - Final Award and Contract Signed	9 days	Thu 12/10/20	Tue 12/22/20																
404	SCG - Submit Advice Letter	0 days	N/A	N/A																
405	SCG - Advice Letter Approved	0 days	N/A	N/A																
406	SCG - Implementation Plan	44 days	Tue 12/22/20	Fri 2/19/21																
407	SCG - Local Large Commercial Solicitation	434 days	Fri 11/1/19	Wed 6/30/21																
408	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20																
409	SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20																
410	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20																
411	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20																
412	SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20																
413	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Mon 6/8/20	Mon 6/8/20																
414	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20																
415	SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20																
416	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20																
417	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20																
418	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
419	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 10/13/20	Tue 10/13/20																
420	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20																
421	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20																
422	SCG - Final Award and Contract Signed	10 days	Thu 12/10/20	Wed 12/23/20																
423	SCG - Submit Advice Letter	64 days	Fri 1/1/21	Wed 3/31/21																
424	SCG - Advice Letter Approved	1 day	Fri 6/4/21	Fri 6/4/21																
425	SCG - Implementation Plan	43 days	Sat 6/5/21	Tue 8/3/21																
426	SCG - Local Agricultural Solicitation	434 days	Fri 11/1/19	Wed 6/30/21																
427	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20																
428	SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20																
429	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20																
430	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20																
431	SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20																
432	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Mon 6/8/20	Mon 6/8/20																
433	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20																
434	SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20																
435	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20																
436	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20																
437	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20																
438	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 10/13/20	Tue 10/13/20																
439	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20																
440	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20																
441	SCG - Final Award and Contract Signed	2 days	Fri 12/11/20	Mon 12/14/20																
442	SCG - Submit Advice Letter	41 days	Fri 1/1/21	Fri 2/26/21																
443	SCG - Advice Letter Approved	1 day	Wed 4/7/21	Wed 4/7/21																
444	SCG - Implementation Plan	43 days	Thu 4/8/21	Mon 6/7/21																
445	SCG - Local Behavioral Solicitation - Residential	413 days?	Fri 5/1/20	Tue 11/30/21																
446	SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20																
447	SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20																
448	SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20																
449	SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20																
450	SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20																
451	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Wed 11/18/20	Wed 11/18/20																
452	SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20																
453	SCG - RFP Release	1 day	Fri 1/15/21	Fri 1/15/21																
454	SCG - RFP Proposal Creation Duration	26 days	Mon 1/18/21	Mon 2/22/21																
455	SCG - RFP Evaluation	29 days	Tue 2/23/21	Fri 4/2/21																
456	SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
457	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 4/13/21	Tue 4/13/21																
458	SCG - Contract Negotiation and Development	95 days	Mon 4/26/21	Fri 9/3/21																
459	SCG - Contract Review with EE PRG	9 days	Tue 9/7/21	Fri 9/17/21																
460	SCG - Final Award and Contract Signed	30 days	Mon 9/20/21	Fri 10/29/21																
461	SCG - Submit Advice Letter	21 days	Mon 11/1/21	Mon 11/29/21																
462	SCG - Advice Letter Approved	1 day	Wed 12/22/21	Wed 12/22/21																
463	SCG - Implementation Plan	43 days	Thu 12/23/21	Sun 2/20/22																
464	SCG - Local Behavioral Solicitation - Commercial	413 days?	Fri 5/1/20	Tue 11/30/21																
465	SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20																
466	SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20																
467	SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20																
468	SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20																
469	SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20																
470	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Wed 11/18/20	Wed 11/18/20																
471	SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20																
472	SCG - RFP Release	1 day	Fri 1/22/21	Fri 1/22/21																
473	SCG - RFP Proposal Creation Duration	26 days	Mon 1/25/21	Mon 3/1/21																
474	SCG - RFP Evaluation	24 days	Tue 3/2/21	Fri 4/2/21																
475	SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21																
476	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Fri 11/12/21	Fri 11/12/21																
477	SCG - Contract Negotiation and Development	132 days	Mon 11/29/21	Tue 5/31/22																
478	SCG - Contract Review with EE PRG	8 days	Sun 6/5/22	Tue 6/14/22																
479	SCG - Final Award and Contract Signed	109 days	Fri 7/1/22	Wed 11/30/22																
480	SCG - Submit Advice Letter	23 days	N/A	N/A																
481	SCG - Advice Letter Approved	1 day	N/A	N/A																
482	SCG - Implementation Plan	43 days	Thu 12/1/22	Sun 1/29/23																
483	SCG - Local Industrial Solicitation	434 days?	Tue 12/1/20	Fri 7/29/22																
484	SCG - RFA Preparation	63 days?	Tue 12/1/20	Thu 2/25/21																
485	SCG - RFA Release	1 day?	Fri 3/19/21	Fri 3/19/21																
486	SCG - RFA Abstract Creation Duration	25 days?	Mon 3/22/21	Fri 4/23/21																
487	SCG - RFA Evaluation	25 days?	Mon 4/26/21	Fri 5/28/21																
488	SCG - RFA Review with EE PRG	1 day?	Tue 6/1/21	Tue 6/1/21																
489	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day?	Tue 6/8/21	Tue 6/8/21																
490	SCG - RFP Preparation	67 days?	Thu 4/1/21	Fri 7/2/21																
491	SCG - RFP Release	1 day?	Fri 7/16/21	Fri 7/16/21																
492	SCG - RFP Proposal Creation Duration	30 days?	Mon 7/19/21	Fri 8/27/21																
493	SCG - RFP Evaluation	25 days?	Mon 8/30/21	Fri 10/1/21																
494	SCG - RFP Review with EE PRG	1 day?	Tue 10/5/21	Tue 10/5/21																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
495	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day?	Tue 12/14/21	Tue 12/14/21																
496	SCG - Contract Negotiation and Development	127 days?	Thu 2/3/22	Fri 7/29/22																
497	SCG - Contract Review with EE PRG	9 days?	Tue 8/2/22	Fri 8/12/22																
498	SCG - Final Award and Contract Signed	21 days?	Fri 7/29/22	Fri 8/26/22																
499	SCG - Submit Advice Letter	1 day?	Sun 10/30/22	Sun 10/30/22																
500	SCG - Advice Letter Approved	1 day?	Mon 1/30/23	Mon 1/30/23																
501	SCG - Implementation Plan	45 days?	Tue 1/31/23	Sat 4/1/23																
502	SCG - Large Public Sector Solicitation (re-Bid)	412 days	Mon 1/4/21	Tue 8/2/22																
503	SCG - RFA Preparation	65 days	Mon 1/4/21	Fri 4/2/21																
504	SCG - RFA Release	1 day	Fri 7/16/21	Fri 7/16/21																
505	SCG - RFA Abstract Creation Duration	20 days	Mon 7/19/21	Fri 8/13/21																
506	SCG - RFA Evaluation	15 days	Mon 8/16/21	Fri 9/3/21																
507	SCG - RFA Review with EE PRG	1 day	Tue 9/7/21	Tue 9/7/21																
508	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 9/14/21	Tue 9/14/21																
509	SCG - RFP Preparation	35 days	Mon 9/13/21	Fri 10/29/21																
510	SCG - RFP Release	1 day	Mon 11/8/21	Mon 11/8/21																
511	SCG - RFP Proposal Creation Duration	29 days	Tue 11/9/21	Fri 12/17/21																
512	SCG - RFP Evaluation	30 days	Mon 12/20/21	Fri 1/28/22																
513	SCG - RFP Review with EE PRG	1 day	Tue 2/1/22	Tue 2/1/22																
514	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 3/8/22	Tue 3/8/22																
515	SCG - Contract Negotiation and Development	79 days	Mon 3/14/22	Thu 6/30/22																
516	SCG - Contract Review with EE PRG	9 days	Tue 7/5/22	Fri 7/15/22																
517	SCG - Final Award and Contract Signed	63 days	Mon 7/18/22	Wed 10/12/22																
518	SCG - Submit Advice Letter	23 days	N/A	N/A																
519	SCG - Advice Letter Approved	1 day	N/A	N/A																
520	SCG - Implementation Plan	44 days	Wed 10/12/22	Sat 12/10/22																
521	SCG - Outreach Solicitation	434 days	Mon 2/1/21	Thu 9/29/22																
522	SCG - RFA Preparation	65 days	Mon 2/1/21	Fri 4/30/21																
523	SCG - RFA Release	1 day	Fri 5/21/21	Fri 5/21/21																
524	SCG - RFA Abstract Creation Duration	25 days	Mon 5/24/21	Fri 6/25/21																
525	SCG - RFA Evaluation	25 days	Mon 6/28/21	Fri 7/30/21																
526	SCG - RFA Review with EE PRG	1 day	Tue 8/3/21	Tue 8/3/21																
527	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 8/10/21	Tue 8/10/21																
528	SCG - RFP Preparation	69 days	Tue 6/1/21	Fri 9/3/21																
529	SCG - RFP Release	1 day	Fri 9/17/21	Fri 9/17/21																
530	SCG - RFP Proposal Creation Duration	30 days	Mon 9/20/21	Fri 10/29/21																
531	SCG - RFP Evaluation	25 days	Mon 11/1/21	Fri 12/3/21																
532	SCG - RFP Review with EE PRG	1 day	Tue 12/7/21	Tue 12/7/21																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
533	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 12/14/21	Tue 12/14/21																
534	SCG - Contract Negotiation and Development	54 days	Mon 1/17/22	Thu 3/31/22																
535	SCG - Contract Review with EE PRG	9 days	Tue 4/5/22	Fri 4/15/22																
536	SCG - Final Award and Contract Signed	10 days	Mon 4/18/22	Fri 4/29/22																
537	SCG - Submit Advice Letter	21 days	N/A	N/A																
538	SCG - Advice Letter Approved	1 day	N/A	N/A																
539	SCG - Implementation Plan	43 days	Sat 4/30/22	Tue 6/28/22																
540	SCG - Marketplace Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22																
541	SCG - RFA Preparation	64 days	Sat 5/1/21	Wed 7/28/21																
542	SCG - RFA Release	1 day	Fri 8/20/21	Fri 8/20/21																
543	SCG - RFA Abstract Creation Duration	25 days	Mon 8/23/21	Fri 9/24/21																
544	SCG - RFA Evaluation	25 days	Mon 9/27/21	Fri 10/29/21																
545	SCG - RFA Review with EE PRG	1 day	Tue 11/2/21	Tue 11/2/21																
546	SCG - RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 11/9/21	Tue 11/9/21																
547	SCG - RFP Preparation	91 days	Thu 8/26/21	Thu 12/30/21																
548	SCG - RFP Release	1 day	Fri 1/14/22	Fri 1/14/22																
549	SCG - RFP Proposal Creation Duration	30 days	Mon 1/17/22	Fri 2/25/22																
550	SCG - RFP Evaluation	25 days	Mon 2/28/22	Fri 4/1/22																
551	SCG - RFP Review with EE PRG	1 day	Tue 5/3/22	Tue 5/3/22																
552	SCG - RFP Estimated Notification of Successful and Unsuccessful Bid	1 day	Wed 5/11/22	Wed 5/11/22																
553	SCG - Contract Negotiation and Development	117 days	Wed 6/22/22	Thu 12/1/22																
554	SCG - Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22																
555	SCG - Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22																
556	SCG - Submit Advice Letter	20 days	Tue 1/3/23	Mon 1/30/23																
557	SCG - Advice Letter Approved	1 day	Tue 5/2/23	Tue 5/2/23																
558	SCG - Implementation Plan	44 days	Wed 5/3/23	Sun 7/2/23																
559	SCG - Residential Multi-Family - Whole Building	436 days?	Mon 3/1/21	Mon 10/31/22																
560	RFA Preparation	40 days	Mon 1/10/22	Fri 3/4/22																
561	RFA Release	1 day	Fri 3/25/22	Fri 3/25/22																
562	RFA Abstract Creation Duration	25 days	Mon 3/28/22	Fri 4/29/22																
563	RFA Evaluation	25 days	Mon 5/2/22	Fri 6/3/22																
564	RFA Review with EE PRG	1 day	Tue 6/7/22	Tue 6/7/22																
565	RFA Estimated Notification of Successful and Unsuccessful Bid	1 day	Tue 6/14/22	Tue 6/14/22																
566	RFP Preparation	28 days	Sun 5/1/22	Tue 6/7/22																
567	RFP Release	1 day	Fri 6/24/22	Fri 6/24/22																
568	RFP Proposal Creation Duration	52 days	Mon 6/27/22	Tue 9/6/22																
569	RFP Evaluation	11 days	Fri 9/9/22	Fri 9/23/22																
570	RFP Review with EE PRG	1 day	Thu 10/6/22	Thu 10/6/22																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
571	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/11/22	Tue 10/11/22																
572	Contract Negotiation and Development	39 days	Tue 10/11/22	Fri 12/2/22																
573	Contract Review with EE PRG	1 day	Tue 12/6/22	Tue 12/6/22																
574	Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22																
575	Submit Advice Letter	22 days	Mon 1/2/23	Tue 1/31/23																
576	Advice Letter Approved	1 day	Fri 3/31/23	Fri 3/31/23																
577	Implementation Plan	43 days	Sat 4/1/23	Tue 5/30/23																
578	SCG – Youth Education Outreach Solicitation	331 days	Tue 3/1/22	Tue 6/6/23																
579	SCG - HERS Rater Training Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22																
580	RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22																
581	RFP Release	1 day	Fri 5/13/22	Fri 5/13/22																
582	RFP Proposal Creation Duration	20 days	Mon 5/16/22	Fri 6/10/22																
583	RFP Evaluation	59 days	Mon 6/13/22	Thu 9/1/22																
584	RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22																
585	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 8/31/22	Wed 8/31/22																
586	Contract Negotiation and Development	53 days	Fri 9/16/22	Tue 11/29/22																
587	Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22																
588	Final Award and Contract Signed	9 days	Mon 12/19/22	Thu 12/29/22																
589	Submit Advice Letter	N/A	N/A	N/A																
590	Advice Letter Approved	N/A	N/A	N/A																
591	Implementation Plan	42 days	Fri 12/30/22	Mon 2/27/23																
592	SCG - Retail Partnering Solicitation	29 days?	Tue 9/27/22	Fri 11/4/22																
593	RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22																
594	RFP Release	1 day	Fri 6/17/22	Fri 6/17/22																
595	RFP Proposal Creation Duration	30 days	Mon 6/20/22	Fri 7/29/22																
596	RFP Evaluation	24 days	Mon 8/1/22	Thu 9/1/22																
597	RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22																
598	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/13/22	Tue 9/13/22																
599	Contract Negotiation and Development	29 days	Mon 9/19/22	Thu 10/27/22																
600	Contract Review with EE PRG	9 days	Tue 11/1/22	Fri 11/11/22																
601	Final Award and Contract Signed	13 days	Mon 11/14/22	Wed 11/30/22																
602	Submit Advice Letter	N/A	N/A	N/A																
603	Advice Letter Approved	N/A	N/A	N/A																
604	Implementation Plan	43 days	Sat 10/1/22	Tue 11/29/22																
605	SCG - Non-Residential EE Advisor Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22																
606	RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22																
607	RFP Release	1 day	Fri 8/26/22	Fri 8/26/22																
608	RFP Proposal Creation Duration	20 days	Mon 8/29/22	Fri 9/23/22																

Project: IOU Master Task Timeli
Date: Fri 8/30/24


Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
609	RFP Evaluation	16 days	Sat 9/24/22	Fri 10/14/22																
610	RFP Review with EE PRG	5 days	Mon 10/17/22	Fri 10/21/22																
611	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/25/22	Tue 10/25/22																
612	Contract Negotiation and Development	32 days	Sun 10/30/22	Mon 12/12/22																
613	Contract Review with EE PRG	9 days	Tue 12/13/22	Fri 12/23/22																
614	Final Award and Contract Signed	4 days	Tue 12/27/22	Fri 12/30/22																
615	Submit Advice Letter	N/A	N/A	N/A																
616	Advice Letter Approved	N/A	N/A	N/A																
617	Implementation Plan	44 days	Sun 1/1/23	Wed 3/1/23																
618	SCG - Residential EE Kits Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22																
619	RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22																
620	RFP Release	1 day	Mon 7/25/22	Mon 7/25/22																
621	RFP Proposal Creation Duration	16 days	Tue 7/26/22	Tue 8/16/22																
622	RFP Evaluation	12 days	Wed 8/17/22	Thu 9/1/22																
623	RFP Review with EE PRG	1 day	Tue 8/2/22	Tue 8/2/22																
624	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/9/22	Tue 8/9/22																
625	Contract Negotiation and Development	30 days	Mon 8/22/22	Fri 9/30/22																
626	Contract Review with EE PRG	9 days	Tue 10/4/22	Fri 10/14/22																
627	Final Award and Contract Signed	10 days	Mon 10/17/22	Fri 10/28/22																
628	Submit Advice Letter	N/A	N/A	N/A																
629	Advice Letter Approved	N/A	N/A	N/A																
630	Implementation Plan	43 days	Sat 10/29/22	Tue 12/27/22																
631	SCG - IDEEA 365	230 days	Mon 2/13/23	Fri 12/29/23																
632	RFP Preparation	23 days	Mon 2/13/23	Wed 3/15/23																
633	RFP Release	20 days	Thu 4/20/23	Wed 5/17/23																
634	RFP Proposal Creation Duration	43 days	Wed 5/3/23	Fri 6/30/23																
635	RFP Evaluation	12 days	Fri 7/14/23	Mon 7/31/23																
636	RFP Review with EE PRG	1 day	Tue 8/1/23	Tue 8/1/23																
637	RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Tue 8/1/23	Thu 8/31/23																
638	Contract Negotiation and Development	21 days	Fri 9/1/23	Fri 9/29/23																
639	Contract Review with EE PRG	32 days	Mon 9/18/23	Tue 10/31/23																
640	Final Award and Contract Signed	17 days	Mon 10/9/23	Tue 10/31/23																
641	Submit Advice Letter	10 days	Wed 11/1/23	Tue 11/14/23																
642	Advice Letter Approved	11 days	Wed 11/22/23	Wed 12/6/23																
643	Implementation Plan	9 days	Tue 12/19/23	Fri 12/29/23																
644	SCG - Commercial SEM	110 days?	Tue 8/1/23	Mon 1/1/24																
645	RFP Preparation	22 days	Tue 8/1/23	Wed 8/30/23																
646	RFP Release	13 days	Wed 9/13/23	Fri 9/29/23																

Project: IOU Master Task Timeli
Date: Fri 8/30/24


Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
647	RFP Proposal Creation Duration	11 days	Mon 10/2/23	Mon 10/16/23																
648	RFP Evaluation	5 days	Wed 10/25/23	Tue 10/31/23																
649	RFP Review with EE PRG	2 days	Tue 10/31/23	Wed 11/1/23																
650	RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Thu 11/2/23	Wed 11/8/23																
651	Contract Negotiation and Development	16 days	Wed 10/25/23	Wed 11/15/23																
652	Contract Review with EE PRG	1 day	Tue 12/5/23	Tue 12/5/23																
653	Final Award and Contract Signed	6 days	Wed 12/13/23	Wed 12/20/23																
654	Submit Advice Letter	5 days	Mon 12/18/23	Fri 12/22/23																
655	Advice Letter Approved	1 day	Fri 12/29/23	Fri 12/29/23																
656	Implementation Plan	1 day	Mon 1/1/24	Mon 1/1/24																
657	<New Task>																			
658																				
659	Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change																			
660	SDG&E - Small Commercial (<20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20																
661	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18																
662	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18																
663	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18																
664	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19																
665	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19																
666	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19																
667	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19																
668	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19																
669	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19																
670	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19																
671	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20																
672	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20																
673	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20																
674	SDG&E - Contract Review with EE PRG	0 days	Tue 6/9/20	Tue 6/9/20																
675	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20																
676	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20																
677	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20																
678	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20																
679	SDG&E - Large Commercial (>20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20																
680	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18																
681	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18																
682	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18																

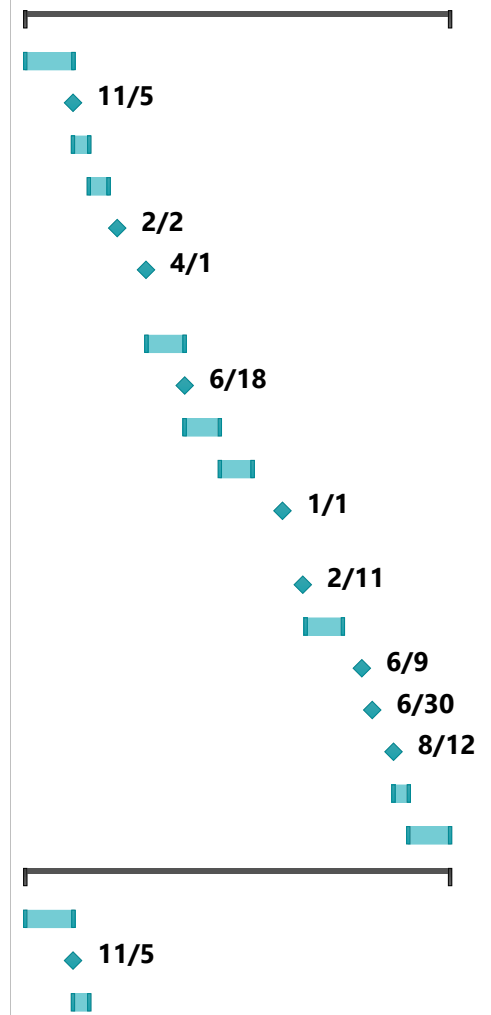

Project: IOU Master Task Timeli Date: Fri 8/30/24	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
683	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19																
684	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19																
685	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19																
686	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19																
687	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19																
688	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19																
689	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19																
690	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20																
691	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20																
692	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20																
693	SDG&E - Contract Review with EE PRG	0 days	Tue 5/12/20	Tue 5/12/20																
694	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20																
695	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20																
696	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20																
697	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20																
698	SDG&E - Residential Multi-Family Solicitation	586 days	Thu 9/6/18	Thu 12/3/20																
699	SDG&E - RFA Preparation	64 days	Thu 9/6/18	Tue 12/4/18																
700	SDG&E - RFA Release	23 days	Tue 12/4/18	Thu 1/3/19																
701	SDG&E - RFA Abstract Creation Duration	49 days	Tue 9/11/18	Fri 11/16/18																
702	SDG&E - RFA Evaluation	21 days	Mon 1/7/19	Mon 2/4/19																
703	SDG&E - RFA Review with EE PRG	0 days	Tue 11/13/18	Tue 11/13/18																
704	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 3/20/19	Wed 3/20/19																
705	SDG&E - RFP Preparation	63 days	Fri 3/22/19	Tue 6/18/19																
706	SDG&E - RFP Release	52 days	Tue 6/18/19	Wed 8/28/19																
707	SDG&E - RFP Proposal Creation Duration	36 days	Mon 3/25/19	Mon 5/13/19																
708	SDG&E - RFP Evaluation	30 days	Thu 8/29/19	Wed 10/9/19																
709	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Thu 12/12/19	Thu 12/19/19																
710	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20																
711	SDG&E - Contract Negotiation and Development	35 days	Mon 4/13/20	Fri 5/29/20																
712	SDG&E - Contract Review with EE PRG	10 days	Thu 6/4/20	Wed 6/17/20																
713	SDG&E - Final Award and Contract Signed	0 days	Mon 6/22/20	Mon 6/22/20																
714	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20																
715	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20																
716	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20																
717	SDG&E - SW HVAC Solicitation	593 days	Thu 11/1/18	Tue 2/9/21																

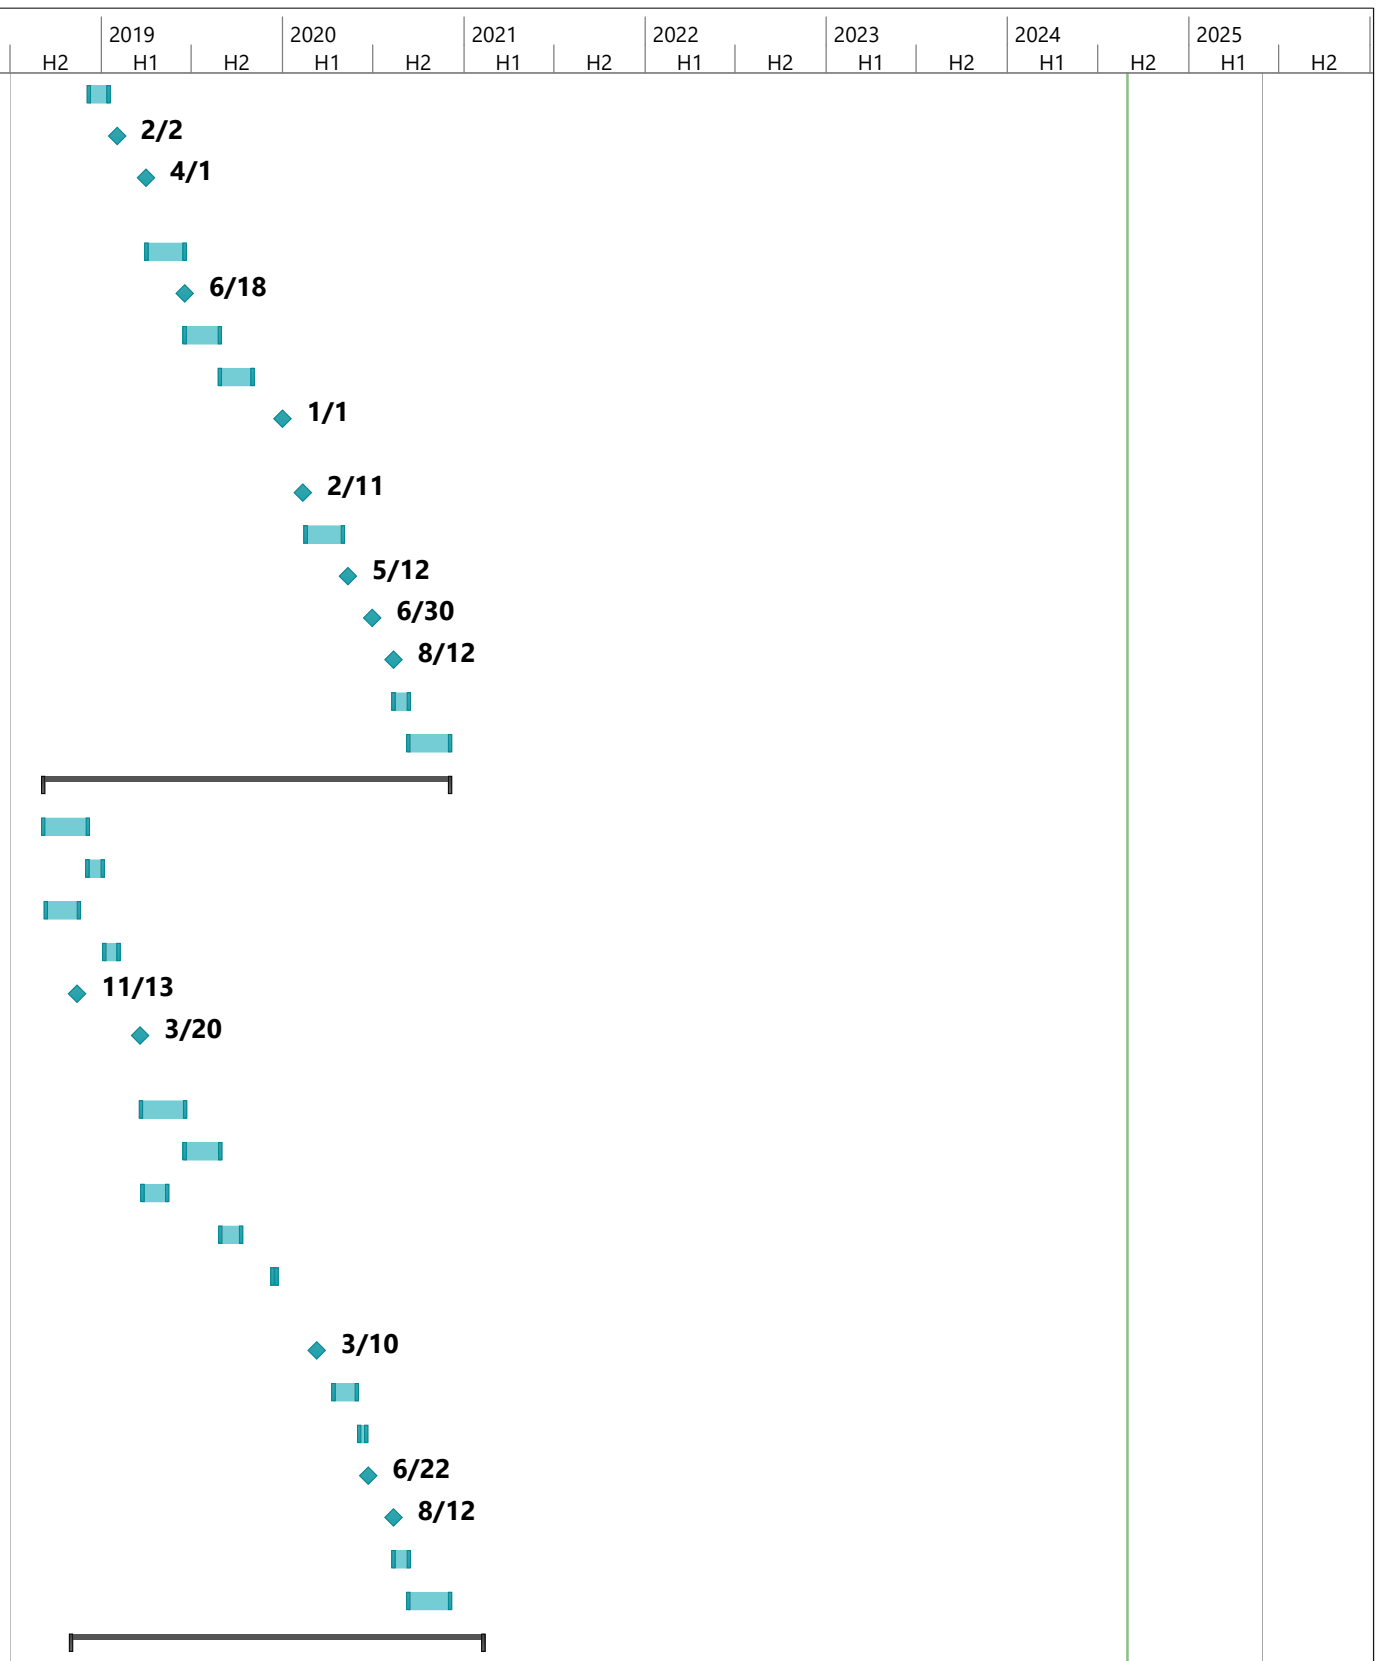

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
718	SDG&E - RFA Preparation	48 days	Thu 11/1/18	Mon 1/7/19																
719	SDG&E - RFA Release	0 days	Mon 1/7/19	Mon 1/7/19			◆ 1/7													
720	SDG&E - RFA Abstract Creation Duration	24 days	Mon 1/7/19	Thu 2/7/19			■													
721	SDG&E - RFA Evaluation	37 days	Fri 2/8/19	Sun 3/31/19			■													
722	SDG&E - RFA Review with EE PRG	0 days	Tue 4/9/19	Tue 4/9/19			◆ 4/9													
723	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 4/17/19	Wed 4/17/19			◆ 4/17													
724	SDG&E - RFP Preparation	73 days	Thu 4/18/19	Mon 7/29/19			■													
725	SDG&E - RFP Release	0 days	Tue 9/3/19	Tue 9/3/19			◆ 9/3													
726	SDG&E - RFP Proposal Creation Duration	30 days	Tue 9/3/19	Mon 10/14/19			■													
727	SDG&E - RFP Evaluation	33 days	Mon 10/14/19	Wed 11/27/19			■													
728	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20			◆ 1/21													
729	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20			◆ 3/10													
730	SDG&E - Contract Negotiation and Development	88 days	Wed 3/25/20	Fri 7/24/20			■													
731	SDG&E - Contract Review with EE PRG	0 days	Tue 9/8/20	Tue 9/8/20			◆ 9/8													
732	SDG&E - Final Award and Contract Signed	0 days	Fri 10/30/20	Fri 10/30/20			◆ 10/30													
733	SDG&E - Submit Advice Letter	0 days	Thu 11/12/20	Thu 11/12/20			◆ 11/12													
734	SDG&E - Advice Letter Approved	0 days	Fri 12/11/20	Fri 12/11/20			◆ 12/11													
735	SDG&E - Implementation Plan	0 days	Tue 2/9/21	Tue 2/9/21			◆ 2/9													
736	SDG&E - SW PLA Solicitation	853 days	Mon 1/28/19	Wed 5/4/22			■													
737	SDG&E - RFA Preparation	75 days	Mon 1/28/19	Fri 5/10/19			■													
738	SDG&E - RFA Release	0 days	Fri 5/10/19	Fri 5/10/19			◆ 5/10													
739	SDG&E - RFA Abstract Creation Duration	31 days	Fri 5/10/19	Fri 6/21/19			■													
740	SDG&E - RFA Evaluation	65 days	Mon 6/24/19	Fri 9/20/19			■													
741	SDG&E - RFA Review with EE PRG	0 days	Tue 9/10/19	Tue 9/10/19			◆ 9/10													
742	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 9/20/19	Fri 9/20/19			◆ 9/20													
743	SDG&E - RFP Preparation	52 days	Fri 9/20/19	Mon 12/2/19			■													
744	SDG&E - RFP Release	0 days	Mon 1/27/20	Mon 1/27/20			◆ 1/27													
745	SDG&E - RFP Proposal Creation Duration	31 days	Mon 1/27/20	Mon 3/9/20			■													
746	SDG&E - RFP Evaluation	82 days	Mon 3/9/20	Tue 6/30/20			■													
747	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 8/17/20	Mon 8/17/20			◆ 8/17													
748	SDG&E - Selection Review with EE PRG	66 days	Tue 10/13/20	Tue 1/12/21			■													
749	SDG&E - Contract Negotiation and Development	197 days	Fri 1/29/21	Mon 11/1/21			■													
750	SDG&E - Contract Review with EE PRG	0 days	Tue 11/9/21	Tue 11/9/21			◆ 11/9													
751	SDG&E - Final Award and Contract Signed	0 days	Fri 1/7/22	Fri 1/7/22			◆ 1/7													
752	SDG&E - Submit Advice Letter	0 days	Mon 1/10/22	Mon 1/10/22			◆ 1/10													

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
753	SDG&E - Advice Letter Approved	0 days	Thu 2/10/22	Thu 2/10/22										◆ 2/10						
754	SDG&E - Implementation Plan	60 days	Thu 2/10/22	Wed 5/4/22										■						
755	SDG&E - Residential Single-Family 2.0 Solicitation	467 days	Tue 1/19/21	Wed 11/2/22										■						
756	SDG&E - RFA Preparation	43 days	Tue 1/19/21	Thu 3/18/21										■						
757	SDG&E - RFA Release	0 days	Mon 3/22/21	Mon 3/22/21										◆ 3/22						
758	SDG&E - RFA Abstract Creation Duration	22 days	Mon 3/22/21	Tue 4/20/21										■						
759	SDG&E - RFA Evaluation	38 days	Wed 4/21/21	Fri 6/11/21										■						
760	SDG&E - RFA Review with EE PRG	7 days	Thu 6/3/21	Fri 6/11/21										■						
761	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 6/15/21	Tue 6/15/21										◆ 6/15						
762	SDG&E - RFP Preparation	43 days	Wed 6/16/21	Fri 8/13/21										■						
763	SDG&E - RFP Release	0 days	Wed 8/18/21	Wed 8/18/21										◆ 8/18						
764	SDG&E - RFP Proposal Creation Duration	32 days	Wed 8/18/21	Thu 9/30/21										■						
765	SDG&E - RFP Evaluation	44 days	Fri 10/1/21	Wed 12/1/21										■						
766	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 12/14/21	Tue 12/14/21										◆ 12/14						
767	SDG&E - Selection Review with EE PRG	7 days	Thu 12/2/21	Fri 12/10/21										■						
768	SDG&E - Contract Negotiation and Development	96 days	Mon 12/20/21	Mon 5/2/22										■						
769	SDG&E - Contract Review with EE PRG	7 days	Thu 5/5/22	Fri 5/13/22										■						
770	SDG&E - Final Award and Contract Signed	0 days	Tue 5/31/22	Tue 5/31/22										◆ 5/31						
771	SDG&E - Submit Advice Letter	0 days	Fri 6/24/22	Fri 6/24/22										◆ 6/24						
772	SDG&E - Advice Letter Approved	0 days	Thu 8/11/22	Thu 8/11/22										◆ 8/11						
773	SDG&E - Implementation Plan	60 days	Thu 8/11/22	Wed 11/2/22										■						
774	SDG&E - Residential Single-Family Solicitation	501 days	Mon 7/1/19	Tue 6/1/21										■						
775	SDG&E - RFA Preparation	80 days	Mon 7/1/19	Fri 10/18/19										■						
776	SDG&E - RFA Release	35 days	Fri 10/18/19	Thu 12/5/19										■						
777	SDG&E - RFA Abstract Creation Duration	53 days	Mon 7/22/19	Wed 10/2/19										■						
778	SDG&E - RFA Evaluation	29 days	Fri 12/6/19	Wed 1/15/20										■						
779	SDG&E - RFA Review with EE PRG	0 days	Tue 10/8/19	Tue 10/8/19										◆ 10/8						
780	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 2/27/20	Thu 2/27/20										◆ 2/27						
781	SDG&E - RFP Preparation	48 days	Fri 2/28/20	Tue 5/5/20										■						
782	SDG&E - RFP Release	0 days	Mon 4/27/20	Mon 4/27/20										◆ 4/27						
783	SDG&E - RFP Proposal Creation Duration	32 days	Mon 4/27/20	Tue 6/9/20										■						
784	SDG&E - RFP Evaluation	16 days	Wed 6/10/20	Wed 7/1/20										■						
785	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	2 days	Thu 7/23/20	Fri 7/24/20										■						
786	SDG&E - Selection Review with EE PRG	7 days	Thu 8/6/20	Fri 8/14/20										■						
787	SDG&E - Contract Negotiation and Development	60 days	Mon 8/17/20	Fri 11/6/20										■						

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task	■	Project Summary	▬	Manual Task	■	Start-only	[Deadline	↓
Split	⋯	Inactive Task	▬	Duration-only	■	Finish-only]	Progress	▬
Milestone	◆	Inactive Milestone	◆	Manual Summary Rollup	■	External Tasks	▬	Manual Progress	▬
Summary	▬	Inactive Summary	▬	Manual Summary	▬	External Milestone	◆		

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
788	SDG&E - Contract Review with EE PRG	10 days	Tue 12/8/20	Mon 12/21/20																
789	SDG&E - Final Award and Contract Signed	0 days	Fri 1/29/21	Fri 1/29/21																
790	SDG&E - Submit Advice Letter	0 days	Mon 3/1/21	Mon 3/1/21																
791	SDG&E - Advice Letter Approved																			
792	SDG&E - Implementation Plan	0 days	Tue 6/1/21	Tue 6/1/21																
793	SDG&E - Public Sector: Federal Solicitation	625 days	Mon 7/1/19	Fri 11/19/21																
794	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19																
795	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19																
796	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19																
797	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20																
798	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20																
799	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20																
800	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20																
801	SDG&E - RFP Release	0 days	Fri 5/22/20	Fri 5/22/20																
802	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20																
803	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20																
804	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20																
805	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20																
806	SDG&E - Contract Negotiation and Development	53 days	Wed 2/17/21	Fri 4/30/21																
807	SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21																
808	SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21																
809	SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21																
810	SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21																
811	SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21																
812	SDG&E - Public Sector: K-12 Solicitation	625 days	Mon 7/1/19	Fri 11/19/21																
813	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19																
814	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19																
815	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19																
816	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20																
817	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20																
818	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20																
819	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20																
820	SDG&E - RFP Release	1 day	Fri 5/22/20	Fri 5/22/20																
821	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20																
822	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
823	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20								◆ 11/18								
824	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20								◆ 11/10								
825	SDG&E - Contract Negotiation and Development	117 days	Thu 11/19/20	Fri 4/30/21								■								
826	SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21								◆ 5/11								
827	SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21								◆ 7/1								
828	SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21								◆ 7/21								
829	SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21								◆ 8/27								
830	SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21								■								
831	SDG&E - Public Sector: Local Government Solicitation	338 days	Tue 10/13/20	Thu 1/27/22								■								
832	SDG&E - RFA Preparation	10 days	Fri 10/23/20	Thu 11/5/20								■								
833	SDG&E - RFA Release	1 day	Wed 1/27/21	Wed 1/27/21																
834	SDG&E - RFA Abstract Creation Duration	20 days	Thu 1/28/21	Wed 2/24/21								■								
835	SDG&E - RFA Evaluation	18 days	Fri 2/26/21	Tue 3/23/21								■								
836	SDG&E - RFA Review with EE PRG	7 days	Thu 4/8/21	Fri 4/16/21																
837	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/21/21	Wed 4/21/21																
838	SDG&E - RFP Preparation	51 days	Fri 3/19/21	Fri 5/28/21								■								
839	SDG&E - RFP Release	1 day	Tue 6/1/21	Tue 6/1/21																
840	SDG&E - RFP Proposal Creation Duration	26 days	Wed 6/2/21	Wed 7/7/21								■								
841	SDG&E - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21								■								
842	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/25/21	Mon 10/25/21																
843	SDG&E - Selection Review with EE PRG	7 days	Tue 10/12/21	Wed 10/20/21																
844	SDG&E - Contract Negotiation and Development	41 days	Fri 11/5/21	Fri 12/31/21								■								
845	SDG&E - Contract Review with EE PRG	7 days	Thu 1/6/22	Fri 1/14/22																
846	SDG&E - Final Award and Contract Signed	9 days	Mon 1/17/22	Thu 1/27/22																
847	SDG&E - Submit Advice Letter	13 days	Wed 6/1/22	Fri 6/17/22								■								
848	SDG&E - Advice Letter Approved	40 days	Fri 6/17/22	Thu 8/11/22								■								
849	SDG&E - Implementation Plan	42 days	Mon 8/15/22	Tue 10/11/22								■								
850	SDG&E - Agricultural Sector: Local Agriculture Solicitation	447 days	Mon 3/1/21	Tue 11/15/22								■								
851	SDG&E - RFA Preparation	56 days	Mon 3/1/21	Mon 5/17/21								■								
852	SDG&E - RFA Release	0 days	Mon 4/26/21	Mon 4/26/21								◆ 4/26								
853	SDG&E - RFA Abstract Creation Duration	20 days	Tue 4/27/21	Mon 5/24/21								■								
854	SDG&E - RFA Evaluation	36 days	Tue 6/1/21	Tue 7/20/21								■								
855	SDG&E - RFA Review with EE PRG	0 days	Thu 7/8/21	Thu 7/8/21								◆ 7/8								
856	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 7/20/21	Tue 7/20/21								◆ 7/20								
857	SDG&E - RFP Preparation	48 days	Tue 7/20/21	Thu 9/23/21								■								

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
858	SDG&E - RFP Release	0 days	Thu 9/23/21	Thu 9/23/21									◆ 9/23							
859	SDG&E - RFP Proposal Creation Duration	25 days	Fri 9/24/21	Thu 10/28/21									■							
860	SDG&E - RFP Evaluation	23 days	Thu 10/28/21	Mon 11/29/21									■							
861	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 2/1/22	Tue 2/1/22									◆ 2/1							
862	SDG&E - Selection Review with EE PRG	0 days	Tue 2/8/22	Tue 2/8/22									◆ 2/8							
863	SDG&E - Contract Negotiation and Development	83 days	Tue 2/1/22	Thu 5/26/22									■							
864	SDG&E - Contract Review with EE PRG	0 days	Tue 6/14/22	Tue 6/14/22									◆ 6/14							
865	SDG&E - Final Award and Contract Signed	10 days	Fri 6/18/21	Thu 7/1/21								■								
866	SDG&E - Submit Advice Letter	0 days	Fri 7/22/22	Fri 7/22/22									◆ 7/22							
867	SDG&E - Advice Letter Approved	0 days	Tue 8/30/22	Tue 8/30/22									◆ 8/30							
868	SDG&E - Implementation Plan	44 days	Wed 8/31/22	Sat 10/29/22									■							
869	*SDG&E - Industrial Solicitation	426 days	Thu 4/1/21	Thu 11/17/22									■							
870	SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21								■								
871	SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21																
872	SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21								■								
873	SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21								■								
874	SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21								■								
875	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21																
876	SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21								■								
877	SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21																
878	SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22								■								
879	SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22								■								
880	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22																
881	SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22								■								
882	SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22								■								
883	SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22																
884	SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22								■								
885	SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22																
886	SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22																
887	SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23								■								
888	*SDG&E - Industrial-Port Tenants Solicitation	426 days	Thu 4/1/21	Thu 11/17/22									■							
889	SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21								■								
890	SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21																
891	SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21								■								
892	SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21								■								
893	SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21								■								

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
894	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21																
895	SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21																
896	SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21																
897	SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22																
898	SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22																
899	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22																
900	SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22																
901	SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22																
902	SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22																
903	SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22																
904	SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22																
905	SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22																
906	SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23																
907	*SDG&E - SW Residential HVAC QI/QM Solicitation	377 days	Mon 7/5/21	Tue 12/13/22																
908	SDG&E - RFA Preparation	48 days	Mon 7/5/21	Wed 9/8/21																
909	SDG&E - RFA Release	1 day	Wed 9/29/21	Wed 9/29/21																
910	SDG&E - RFA Abstract Creation Duration	22 days	Wed 9/29/21	Thu 10/28/21																
911	SDG&E - RFA Evaluation	21 days	Fri 10/29/21	Fri 11/26/21																
912	SDG&E - RFA Review with EE PRG	6 days	Fri 12/10/21	Fri 12/17/21																
913	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 12/22/21	Wed 12/22/21																
914	SDG&E - RFP Preparation	56 days	Tue 1/4/22	Tue 3/22/22																
915	SDG&E - RFP Release	1 day	Tue 3/22/22	Tue 3/22/22																
916	SDG&E - RFP Proposal Creation Duration	23 days	Wed 3/23/22	Fri 4/22/22																
917	SDG&E - RFP Evaluation	20 days	Mon 4/25/22	Fri 5/20/22																
918	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/21/22	Tue 6/21/22																
919	SDG&E - Selection Review with EE PRG	0 days	Fri 6/17/22	Fri 6/17/22																
920	SDG&E - Contract Negotiation and Development	83 days	Wed 7/20/22	Fri 11/11/22																
921	SDG&E - Contract Review with EE PRG	6 days	Mon 11/14/22	Mon 11/21/22																
922	SDG&E - Final Award and Contract Signed	1 day	Mon 1/10/22	Mon 1/10/22																
923	SDG&E - Submit Advice Letter	22 days	Sun 1/15/23	Mon 2/13/23																
924	SDG&E - Advice Letter Approved	1 day	Fri 4/28/23	Fri 4/28/23																
925	SDG&E - Implementation Plan	60 days	Fri 4/28/23	Thu 7/20/23																
926	*SDG&E - Local/Residential Behavioral Solicitation	472 days	Mon 4/19/21	Tue 2/7/23																
927	SDG&E - RFA Preparation	53 days	Mon 4/19/21	Wed 6/30/21																
928	SDG&E - RFA Release	1 day	Mon 7/26/21	Mon 7/26/21																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
929	SDG&E - RFA Abstract Creation Duration	21 days	Mon 7/26/21	Mon 8/23/21																
930	SDG&E - RFA Evaluation	30 days	Tue 8/24/21	Mon 10/4/21																
931	SDG&E - RFA Review with EE PRG	7 days	Thu 10/7/21	Fri 10/15/21																
932	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/19/21	Tue 10/19/21																
933	SDG&E - RFP Preparation	28 days	Thu 10/21/21	Mon 11/29/21																
934	SDG&E - RFP Release	1 day	Wed 12/22/21	Wed 12/22/21																
935	SDG&E - RFP Proposal Creation Duration	20 days	Wed 12/22/21	Tue 1/18/22																
936	SDG&E - RFP Evaluation	28 days	Wed 1/19/22	Fri 2/25/22																
937	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/15/22	Tue 3/15/22																
938	SDG&E - Selection Review with EE PRG	7 days	Thu 3/3/22	Fri 3/11/22																
939	SDG&E - Contract Negotiation and Development	119 days	Fri 3/18/22	Wed 8/31/22																
940	SDG&E - Contract Review with EE PRG	7 days	Thu 9/8/22	Fri 9/16/22																
941	SDG&E - Final Award and Contract Signed	1 day	Fri 10/21/22	Fri 10/21/22																
942	SDG&E - Submit Advice Letter	1 day	Wed 11/16/22	Wed 11/16/22																
943	SDG&E - Advice Letter Approved	1 day	Fri 12/16/22	Fri 12/16/22																
944	SDG&E - Implementation Plan	60 days	Wed 11/16/22	Tue 2/7/23																
945	*SDG&E - Small Business Outreach Solicitation	298 days?	Wed 4/13/22	Fri 6/2/23																
946	SDG&E - RFA Preparation	53 days	Wed 4/13/22	Fri 6/24/22																
947	SDG&E - RFA Release	1 day	Thu 7/7/22	Thu 7/7/22																
948	SDG&E - RFA Abstract Creation Duration	21 days	Fri 7/8/22	Fri 8/5/22																
949	SDG&E - RFA Evaluation	30 days	Mon 8/8/22	Fri 9/16/22																
950	SDG&E - RFA Review with EE PRG	5 days	Mon 9/19/22	Fri 9/23/22																
951	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/27/22	Tue 9/27/22																
952	SDG&E - RFP Preparation	28 days	Mon 8/8/22	Wed 9/14/22																
953	SDG&E - RFP Release	1 day	Tue 10/18/22	Tue 10/18/22																
954	SDG&E - RFP Proposal Creation Duration	31 days	Tue 10/18/22	Tue 11/29/22																
955	SDG&E - RFP Evaluation	38 days	Wed 11/30/22	Fri 1/20/23																
956	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 2/28/23	Tue 2/28/23																
957	SDG&E - Selection Review with EE PRG	7 days	Thu 2/16/23	Fri 2/24/23																
958	SDG&E - Contract Negotiation and Development	79 days	Tue 2/28/23	Fri 6/16/23																
959	SDG&E - Contract Review with EE PRG	4 days	Wed 6/21/23	Mon 6/26/23																
960	SDG&E - Final Award and Contract Signed	1 day	Tue 8/29/23	Tue 8/29/23																
961	SDG&E - Submit Advice Letter	1 day	Fri 9/15/23	Fri 9/15/23																
962	SDG&E - Advice Letter Approved	1 day	Mon 10/16/23	Mon 10/16/23																
963	SDG&E - Implementation Plan	46 days	Mon 10/16/23	Mon 12/18/23																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
964	*SDG&E - Workforce Education & Training /Integrated Energy Education Solicitation	353 days?	Mon 1/16/23	Wed 5/22/24																
965	SDG&E - RFP Release	1 day?	Thu 2/2/23	Thu 2/2/23																
966	SDG&E - RFP Evaluation	25 days	Fri 3/17/23	Thu 4/20/23																
967	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/16/23	Tue 5/16/23																
968	SDG&E - Selection Review with EE PRG	5 days	Tue 5/9/23	Mon 5/15/23																
969	SDG&E - Contract Negotiation and Development	94 days	Fri 5/5/23	Wed 9/13/23																
970	SDG&E - Contract Review with EE PRG	7 days	Tue 10/10/23	Wed 10/18/23																
971	SDG&E - Final Award and Contract Signed	1 day	Tue 11/14/23	Tue 11/14/23																
972	SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24																
973	SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24																
974	SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24																
975	*SDG&E - Residential Equity Education & Outreach Solicitation	331 days?	Fri 1/13/23	Fri 4/19/24																
976	SDG&E - RFA Release	1 day	Thu 3/2/23	Thu 3/2/23																
977	SDG&E - RFA Evaluation	21 days	Wed 4/12/23	Wed 5/10/23																
978	SDG&E - RFA Review with EE PRG	7 days	Fri 5/19/23	Mon 5/29/23																
979	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/30/23	Tue 5/30/23																
980	SDG&E - RFP Release	1 day	Thu 6/1/23	Thu 6/1/23																
981	SDG&E - RFP Evaluation	27 days	Mon 7/17/23	Tue 8/22/23																
982	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/28/23	Mon 8/28/23																
983	SDG&E - Selection Review with EE PRG	7 days	Wed 8/30/23	Thu 9/7/23																
984	SDG&E - Contract Negotiation and Development	32 days	Thu 11/2/23	Fri 12/15/23																
985	SDG&E - Contract Review with EE PRG	7 days	Tue 1/9/24	Wed 1/17/24																
986	SDG&E - Final Award and Contract Signed	1 day	Mon 2/12/24	Mon 2/12/24																
987	SDG&E - Submit Advice Letter	1 day	Mon 2/26/24	Mon 2/26/24																
988	SDG&E - Advice Letter Approved	1 day	Mon 4/8/24	Mon 4/8/24																
989	SDG&E - Implementation Plan	60 days	Tue 4/9/24	Mon 7/1/24																
990	*SDG&E - Non-Residential Behavioral Solicitation	398 days	Mon 8/15/22	Wed 2/21/24																
991	SDG&E - RFA Preparation	67 days	Mon 8/15/22	Tue 11/15/22																
992	SDG&E - RFA Release	1 day	Mon 10/24/22	Mon 10/24/22																
993	SDG&E - RFA Abstract Creation Duration	27 days	Tue 8/23/22	Wed 9/28/22																
994	SDG&E - RFA Evaluation	16 days	Tue 11/29/22	Tue 12/20/22																
995	SDG&E - RFA Review with EE PRG	7 days	Thu 1/5/23	Fri 1/13/23																
996	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 1/18/23	Wed 1/18/23																
997	SDG&E - RFP Preparation	26 days	Mon 11/14/22	Mon 12/19/22																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
998	SDG&E - RFP Release	1 day	Mon 1/23/23	Mon 1/23/23																
999	SDG&E - RFP Proposal Creation Duration	26 days	Mon 1/23/23	Mon 2/27/23																
1000	SDG&E - RFP Evaluation	58 days	Tue 2/28/23	Thu 5/18/23																
1001	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/20/23	Tue 6/20/23																
1002	SDG&E - Selection Review with EE PRG	7 days	Thu 6/8/23	Fri 6/16/23																
1003	SDG&E - Contract Negotiation and Development	60 days	Wed 6/21/23	Tue 9/12/23																
1004	SDG&E - Contract Review with EE PRG	7 days	Thu 10/5/23	Fri 10/13/23																
1005	SDG&E - Final Award and Contract Signed	1 day	Thu 12/21/23	Thu 12/21/23																
1006	SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24																
1007	SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24																
1008	SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24																
1009	*SDG&E - Retail Offices and Wholesale Solicitation	398 days	Wed 5/10/23	Fri 11/15/24																
1010	SDG&E - RFA Preparation	33 days	Wed 5/10/23	Fri 6/23/23																
1011	SDG&E - RFA Release	1 day	Mon 7/3/23	Mon 7/3/23																
1012	SDG&E - RFA Abstract Creation Duration	31 days	Tue 7/4/23	Tue 8/15/23																
1013	SDG&E - RFA Evaluation	19 days	Wed 8/16/23	Mon 9/11/23																
1014	SDG&E - RFA Review with EE PRG	3 days	Mon 9/18/23	Wed 9/20/23																
1015	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 9/25/23	Mon 9/25/23																
1016	SDG&E - RFP Preparation	33 days	Wed 7/5/23	Fri 8/18/23																
1017	SDG&E - RFP Release	1 day	Fri 9/29/23	Fri 9/29/23																
1018	SDG&E - RFP Proposal Creation Duration	33 days	Mon 10/2/23	Wed 11/15/23																
1019	SDG&E - RFP Evaluation	25 days	Thu 11/16/23	Wed 12/20/23																
1020	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 2/19/24	Mon 2/19/24																
1021	SDG&E - Selection Review with EE PRG	7 days	Thu 2/8/24	Fri 2/16/24																
1022	SDG&E - Contract Negotiation and Development	96 days	Mon 2/26/24	Mon 7/8/24																
1023	SDG&E - Contract Review with EE PRG	6 days	Wed 7/17/24	Wed 7/24/24																
1024	SDG&E - Final Award and Contract Signed	1 day	Tue 8/27/24	Tue 8/27/24																
1025	SDG&E - Submit Advice Letter	1 day	Fri 9/13/24	Fri 9/13/24																
1026	SDG&E - Advice Letter Approved	1 day	Mon 10/14/24	Mon 10/14/24																
1027	SDG&E - Implementation Plan	46 days	Mon 10/14/24	Mon 12/16/24																
1028	*SDG&E - Groceries, Restaurants and Food Storage Solicitation	398 days	Wed 6/14/23	Fri 12/20/24																
1029	SDG&E - RFA Preparation	33 days	Wed 6/14/23	Fri 7/28/23																
1030	SDG&E - RFA Release	1 day	Tue 8/15/23	Tue 8/15/23																
1031	SDG&E - RFA Abstract Creation Duration	21 days	Wed 8/16/23	Wed 9/13/23																
1032	SDG&E - RFA Evaluation	15 days	Thu 9/14/23	Wed 10/4/23																
1033	SDG&E - RFA Review with EE PRG	5 days	Wed 10/18/23	Tue 10/24/23																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1034	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/30/23	Mon 10/30/23																
1035	SDG&E - RFP Preparation	16 days	Mon 10/9/23	Mon 10/30/23																
1036	SDG&E - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23																
1037	SDG&E - RFP Proposal Creation Duration	33 days	Mon 11/6/23	Wed 12/20/23																
1038	SDG&E - RFP Evaluation	34 days	Thu 12/21/23	Tue 2/6/24																
1039	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/22/24	Thu 2/22/24																
1040	SDG&E - Selection Review with EE PRG	7 days	Thu 2/29/24	Fri 3/8/24																
1041	SDG&E - Contract Negotiation and Development	60 days	Tue 2/27/24	Mon 5/20/24																
1042	SDG&E - Contract Review with EE PRG	9 days	Thu 6/27/24	Tue 7/9/24																
1043	SDG&E - Final Award and Contract Signed	1 day	Mon 7/15/24	Mon 7/15/24																
1044	SDG&E - Submit Advice Letter	1 day	Mon 7/22/24	Mon 7/22/24																
1045	SDG&E - Advice Letter Approved	1 day	Tue 9/3/24	Tue 9/3/24																
1046	SDG&E - Implementation Plan	60 days	Wed 9/4/24	Tue 11/26/24																
1047	*SDG&E - Private Institutions and Healthcare Solicitation	398 days	Thu 10/5/23	Mon 4/14/25																
1048	SDG&E - RFA Preparation	33 days	Thu 10/5/23	Mon 11/20/23																
1049	SDG&E - RFA Release	1 day	Mon 11/27/23	Mon 11/27/23																
1050	SDG&E - RFA Abstract Creation Duration	35 days	Mon 11/27/23	Fri 1/12/24																
1051	SDG&E - RFA Evaluation	30 days	Mon 1/15/24	Fri 2/23/24																
1052	SDG&E - RFA Review with EE PRG	5 days	Mon 2/26/24	Fri 3/1/24																
1053	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 3/4/24	Mon 3/4/24																
1054	SDG&E - RFP Preparation	54 days	Mon 11/27/23	Thu 2/8/24																
1055	SDG&E - RFP Release	1 day	Fri 3/8/24	Fri 3/8/24																
1056	SDG&E - RFP Proposal Creation Duration	34 days	Fri 3/8/24	Wed 4/24/24																
1057	SDG&E - RFP Evaluation	42 days	Thu 4/25/24	Fri 6/21/24																
1058	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 7/2/24	Tue 7/2/24																
1059	SDG&E - Selection Review with EE PRG	7 days	Fri 6/21/24	Mon 7/1/24																
1060	SDG&E - Contract Negotiation and Development	55 days	Mon 7/15/24	Fri 9/27/24																
1061	SDG&E - Contract Review with EE PRG	7 days	Thu 10/3/24	Fri 10/11/24																
1062	SDG&E - Final Award and Contract Signed	1 day	Fri 11/15/24	Fri 11/15/24																
1063	SDG&E - Submit Advice Letter	1 day	Wed 11/27/24	Wed 11/27/24																
1064	SDG&E - Advice Letter Approved	1 day	Fri 12/27/24	Fri 12/27/24																
1065	SDG&E - Implementation Plan	46 days	Mon 12/30/24	Mon 3/3/25																
1066	*SDG&E - Lodging: Hotels/Motels Solicitation	398 days	Tue 10/10/23	Thu 4/17/25																
1067	SDG&E - RFA Preparation	33 days	Tue 10/10/23	Thu 11/23/23																
1068	SDG&E - RFA Release	1 day	Fri 12/8/23	Fri 12/8/23																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1069	SDG&E - RFA Abstract Creation Duration	35 days	Fri 12/8/23	Thu 1/25/24																
1070	SDG&E - RFA Evaluation	22 days	Mon 1/22/24	Tue 2/20/24																
1071	SDG&E - RFA Review with EE PRG	7 days	Tue 3/12/24	Wed 3/20/24																
1072	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/19/24	Tue 3/19/24																
1073	SDG&E - RFP Preparation	48 days	Tue 1/23/24	Thu 3/28/24																
1074	SDG&E - RFP Release	1 day	Thu 3/21/24	Thu 3/21/24																
1075	SDG&E - RFP Proposal Creation Duration	29 days	Thu 3/21/24	Tue 4/30/24																
1076	SDG&E - RFP Evaluation	23 days	Mon 5/6/24	Wed 6/5/24																
1077	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/18/24	Tue 6/18/24																
1078	SDG&E - Selection Review with EE PRG	7 days	Thu 6/20/24	Fri 6/28/24																
1079	SDG&E - Contract Negotiation and Development	60 days	Wed 7/17/24	Tue 10/8/24																
1080	SDG&E - Contract Review with EE PRG	9 days	Thu 11/7/24	Tue 11/19/24																
1081	SDG&E - Final Award and Contract Signed	1 day	Tue 11/19/24	Tue 11/19/24																
1082	SDG&E - Submit Advice Letter	1 day	Mon 1/6/25	Mon 1/6/25																
1083	SDG&E - Advice Letter Approved	1 day	Thu 2/6/25	Thu 2/6/25																
1084	SDG&E - Implementation Plan	46 days	Fri 3/21/25	Fri 5/23/25																
1085	*SDG&E - Market Access Program (MAP)	317 days	Wed 3/13/24	Thu 5/29/25																
1086	SDG&E - RFP Preparation	38 days	Wed 3/13/24	Fri 5/3/24																
1087	SDG&E - RFP Release	1 day	Tue 5/7/24	Tue 5/7/24																
1088	SDG&E - RFP Proposal Creation Duration	31 days	Tue 5/7/24	Tue 6/18/24																
1089	SDG&E - RFP Evaluation	43 days	Wed 6/19/24	Fri 8/16/24																
1090	SDG&E - Selection Review with EE PRG	7 days	Thu 9/5/24	Fri 9/13/24																
1091	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/17/24	Tue 9/17/24																
1092	SDG&E - Contract Negotiation and Development	60 days	Fri 9/27/24	Thu 12/19/24																
1093	SDG&E - Contract Review with EE PRG	7 days	Thu 1/9/25	Fri 1/17/25																
1094	SDG&E - Final Award and Contract Signed	1 day	Fri 1/31/25	Fri 1/31/25																
1095	SDG&E - Submit Advice Letter	1 day	Fri 2/14/25	Fri 2/14/25																
1096	SDG&E - Advice Letter Approved	1 day	Mon 3/31/25	Mon 3/31/25																
1097	SDG&E - Implementation Plan	44 days	Mon 3/31/25	Thu 5/29/25																
1098	Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change																			
1099																				
1100	PG&E - Local Government Partnerships (non-resource programs) Solicitation	376 days?	Fri 3/22/19	Fri 8/28/20																
1101	PG&E - RFA Preparation	42 days	Fri 3/22/19	Mon 5/20/19																
1102	PG&E - RFA Release	1 day	Thu 5/23/19	Thu 5/23/19																

Project: IOU Master Task Timeli
Date: Fri 8/30/24


Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1103	PG&E - RFA Abstract Creation Duration	22 days	Thu 5/23/19	Fri 6/21/19																
1104	PG&E - RFA Evaluation	15 days	Mon 6/24/19	Fri 7/12/19																
1105	PG&E - RFA Review with EE PRG	4 days	Tue 7/23/19	Fri 7/26/19																
1106	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/5/19	Fri 8/9/19																
1107	PG&E - RFP Preparation	45 days	Tue 8/27/19	Mon 10/28/19																
1108	PG&E - RFP Release	1 day	Mon 11/4/19	Mon 11/4/19																
1109	PG&E - RFP Proposal Creation Duration	33 days	Mon 11/4/19	Wed 12/18/19																
1110	PG&E - RFP Evaluation	18 days	Mon 1/6/20	Wed 1/29/20																
1111	PG&E - RFP Review with EE PRG	4 days	Tue 2/25/20	Fri 2/28/20																
1112	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/2/20	Fri 3/6/20																
1113	PG&E - Contract Negotiation and Development	58 days	Fri 2/28/20	Tue 5/19/20																
1114	PG&E - Contract Review with EE PRG	7 days	Tue 5/26/20	Wed 6/3/20																
1115	PG&E - Final Award and Contract Signed	22 days	Fri 5/29/20	Mon 6/29/20																
1116	PG&E - Submit Advice Letter		N/A	N/A																
1117	PG&E - Advice Letter Approved																			
1118	PG&E - Implementation Plan	24 days	Tue 7/28/20	Fri 8/28/20																
1119	PG&E - Statewide Codes & Standards (RFP only) Solicitation	221 days?	Mon 7/8/19	Mon 5/11/20																
1120	PG&E - RFA Preparation		N/A	N/A																
1121	PG&E - RFA Release		N/A	N/A																
1122	PG&E - RFA Abstract Creation Duration		N/A	N/A																
1123	PG&E - RFA Evaluation		N/A	N/A																
1124	PG&E - RFA Review with EE PRG		N/A	N/A																
1125	PG&E - RFA Estimated Notification of Successful and Unsuccessful		N/A	N/A																
1126	PG&E - RFP Preparation	36 days	Mon 7/8/19	Mon 8/26/19																
1127	PG&E - RFP Release	1 day	Tue 9/10/19	Tue 9/10/19																
1128	PG&E - RFP Proposal Creation Duration	24 days	Tue 9/10/19	Fri 10/11/19																
1129	PG&E - RFP Evaluation	10 days	Mon 10/14/19	Fri 10/25/19																
1130	PG&E - RFP Review with EE PRG	4 days	Thu 11/21/19	Tue 11/26/19																
1131	PG&E - RFP Estimated Notification of Successful and Unsuccessful	3 days	Wed 11/27/19	Fri 11/29/19																
1132	PG&E - Contract Negotiation and Development	35 days	Mon 12/2/19	Fri 1/17/20																
1133	PG&E - Contract Review with EE PRG	4 days	Tue 1/21/20	Fri 1/24/20																
1134	PG&E - Final Award and Contract Signed	32 days	Wed 1/29/20	Thu 3/12/20																
1135	PG&E - Submit Advice Letter		N/A	N/A																
1136	PG&E - Advice Letter Approved																			
1137	PG&E - Implementation Plan	32 days	Fri 3/27/20	Mon 5/11/20																
1138	PG&E - Local Multi-Sector (40% outsource) Solicitation	251 days?	Tue 4/28/20	Tue 4/13/21																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1139	PG&E - RFA Preparation		N/A	N/A																
1140	PG&E - RFA Release		N/A	N/A																
1141	PG&E - RFA Abstract Creation Duration		N/A	N/A																
1142	PG&E - RFA Evaluation		N/A	N/A																
1143	PG&E - RFA Review with EE PRG		N/A	N/A																
1144	PG&E - RFA Estimated Notification of Successful and Unsuccessful		N/A	N/A																
1145	PG&E - RFP Preparation		N/A	N/A																
1146	PG&E - RFP Release		N/A	N/A																
1147	PG&E - RFP Proposal Creation Duration		N/A	N/A																
1148	PG&E - RFP Evaluation		N/A	N/A																
1149	PG&E - RFP Review with EE PRG	4 days	Tue 4/28/20	Fri 5/1/20																
1150	PG&E - RFP Estimated Notification of Successful and Unsuccessful																			
1151	PG&E - Contract Negotiation and Development	81 days	Thu 7/2/20	Thu 10/22/20																
1152	PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20																
1153	PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20																
1154	PG&E - Submit Advice Letter	1 day	Wed 1/13/21	Wed 1/13/21																
1155	PG&E - Advice Letter Approved	1 day?	Fri 2/12/21	Fri 2/12/21																
1156	PG&E - Implementation Plan	43 days	Sat 2/13/21	Tue 4/13/21																
1157	PG&E - Statewide New Constructions (Non-Residential) Solicitation	591 days	Mon 3/25/19	Sun 6/27/21																
1158	PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19																
1159	PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19																
1160	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19																
1161	PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19																
1162	PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19																
1163	PG&E - RFA Estimated Notification of Successful and Unsuccessful	4 days	Tue 8/27/19	Fri 8/30/19																
1164	PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20																
1165	PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20																
1166	PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20																
1167	PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20																
1168	PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20																
1169	PG&E - RFP Estimated Notification of Successful and Unsuccessful	6 days	Wed 8/5/20	Wed 8/12/20																
1170	PG&E - Contract Negotiation and Development	49 days	Mon 8/17/20	Thu 10/22/20																
1171	PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20																
1172	PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20																
1173	PG&E - Submit Advice Letter	1 day	Fri 2/19/21	Fri 2/19/21																
1174	PG&E - Advice Letter Approved	1 day	Wed 4/28/21	Wed 4/28/21																
1175	PG&E - Implementation Plan	43 days	Thu 4/29/21	Sun 6/27/21																
1176	PG&E - Statewide New Construction (Residential) Solicitation	640 days?	Mon 3/25/19	Fri 9/3/21																

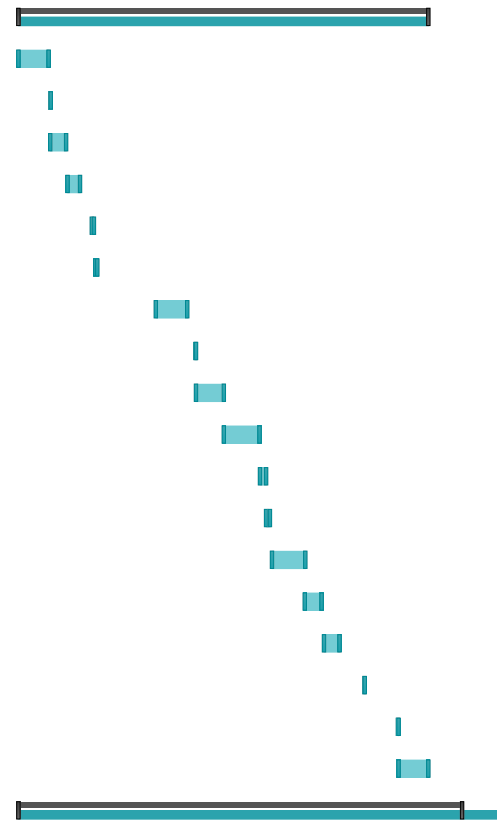

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1177	PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19																
1178	PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19																
1179	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19																
1180	PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19																
1181	PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19																
1182	PG&E - RFA Estimated Notification of Successful and Unsuccessful	4 days	Tue 8/27/19	Fri 8/30/19																
1183	PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20																
1184	PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20																
1185	PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20																
1186	PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20																
1187	PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20																
1188	PG&E - RFP Estimated Notification of Successful and Unsuccessful	6 days	Wed 8/5/20	Wed 8/12/20																
1189	PG&E - Contract Negotiation and Development	177 days	Mon 8/17/20	Tue 4/20/21																
1190	PG&E - Contract Review with EE PRG	16 days	Thu 4/22/21	Thu 5/13/21																
1191	PG&E - Final Award and Contract Signed	32 days	Sat 5/15/21	Mon 6/28/21																
1192	PG&E - Submit Advice Letter	1 day	Mon 7/12/21	Mon 7/12/21																
1193	PG&E - Advice Letter Approved (all electric)	1 day	Wed 8/11/21	Wed 8/11/21																
1194	PG&E - Advice Letter Approved (mixed fuel)	1 day	Wed 9/15/21	Wed 9/15/21																
1195	PG&E - Implementation Plan (all electric)	43 days	Thu 8/12/21	Mon 10/11/21																
1196	PG&E - Implementation Plan (mixed fuel)	43 days	Thu 9/16/21	Sun 11/14/21																
1197	PG&E - Statewide WE&T Career Connections Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21																
1198	PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20																
1199	PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20																
1200	PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20																
1201	PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20																
1202	PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20																
1203	PG&E - RFA Estimated Notification of Successful and Unsuccessful	4 days	Fri 7/3/20	Wed 7/8/20																
1204	PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20																
1205	PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20																
1206	PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20																
1207	PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20																
1208	PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20																
1209	PG&E - RFP Estimated Notification of Successful and Unsuccessful	1 day	Tue 11/10/20	Tue 11/10/20																
1210	PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21																
1211	PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21																
1212	PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21																
1213	PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21																
1214	PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1215	PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21																
1216	PG&E - Statewide WE&T Career and Workforce Readiness Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21																
1217	PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20																
1218	PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20																
1219	PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20																
1220	PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20																
1221	PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20																
1222	PG&E - RFA Estimated Notification of Successful and Unsuccessful	4 days	Fri 7/3/20	Wed 7/8/20																
1223	PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20																
1224	PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20																
1225	PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20																
1226	PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20																
1227	PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20																
1228	PG&E - RFP Estimated Notification of Successful and Unsuccessful	1 day	Tue 11/10/20	Tue 11/10/20																
1229	PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21																
1230	PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21																
1231	PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21																
1232	PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21																
1233	PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21																
1234	PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21																
1235	PG&E - Statewide State of CA (Dept. of Corrections) Solicitation	348 days?	Sun 3/1/20	Tue 6/29/21																
1236	PG&E - RFA Preparation	46 days	Sun 3/1/20	Fri 5/1/20																
1237	PG&E - RFA Release	1 day	Wed 5/13/20	Wed 5/13/20																
1238	PG&E - RFA Abstract Creation Duration	31 days	Wed 5/13/20	Wed 6/24/20																
1239	PG&E - RFA Evaluation	15 days	Mon 6/29/20	Fri 7/17/20																
1240	PG&E - RFA Review with EE PRG	5 days	Tue 7/28/20	Mon 8/3/20																
1241	PG&E - RFA Estimated Notification of Successful and Unsuccessful	5 days	Mon 8/3/20	Fri 8/7/20																
1242	PG&E - RFP Preparation	20 days	Mon 8/3/20	Fri 8/28/20																
1243	PG&E - RFP Release	1 day	Wed 9/9/20	Wed 9/9/20																
1244	PG&E - RFP Proposal Creation Duration	31 days	Wed 9/9/20	Wed 10/21/20																
1245	PG&E - RFP Evaluation	31 days	Fri 10/23/20	Fri 12/4/20																
1246	PG&E - RFP Review with EE PRG	6 days	Tue 12/22/20	Tue 12/29/20																
1247	PG&E - RFP Estimated Notification of Successful and Unsuccessful	3 days	Wed 1/6/21	Fri 1/8/21																
1248	PG&E - Contract Negotiation and Development	65 days	Wed 1/20/21	Tue 4/20/21																
1249	PG&E - Contract Review with EE PRG	7 days	Thu 4/22/21	Fri 4/30/21																
1250	PG&E - Final Award and Contract Signed	22 days	Sat 5/1/21	Mon 5/31/21																
1251	PG&E - Submit Advice Letter	1 day	Thu 6/24/21	Thu 6/24/21																
1252	PG&E - Advice Letter Approved	1 day	Wed 7/28/21	Wed 7/28/21																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1253	PG&E - Implementation Plan	43 days	Thu 7/29/21	Sun 9/26/21																
1254	PG&E - Local (Micro and Small Business Equity Program) Solicitation	403 days?	Tue 6/1/21	Thu 12/15/22																
1255	PG&E - RFA Preparation	38 days	Tue 6/1/21	Thu 7/22/21																
1256	PG&E - RFA Release	1 day	Tue 9/7/21	Tue 9/7/21																
1257	PG&E - RFA Abstract Creation Duration	34 days	Wed 9/8/21	Mon 10/25/21																
1258	PG&E - RFA Evaluation	18 days	Tue 10/26/21	Thu 11/18/21																
1259	PG&E - RFP Release	1 day	Wed 12/8/21	Wed 12/8/21																
1260	PG&E - RFP Proposal Creation Duration	46 days	Wed 12/8/21	Wed 2/9/22																
1261	PG&E - RFP Evaluation	21 days	Thu 2/10/22	Thu 3/10/22																
1262	PG&E - RFP Review with EE PRG	6 days	Thu 3/17/22	Thu 3/24/22																
1263	PG&E - RFP Estimated Bidder Notification	1 day	Wed 3/30/22	Wed 3/30/22																
1264	PG&E - Contract Negotiation and Development	71 days	Thu 4/7/22	Thu 7/14/22																
1265	PG&E - Contract Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22																
1266	PG&E - Final Award and Contract Signed	45 days	Mon 8/8/22	Fri 10/7/22																
1267	PG&E - Submit Advice Letter	1 day	Wed 10/12/22	Wed 10/12/22																
1268	PG&E - Advice Letter Approved	1 day	Fri 11/11/22	Fri 11/11/22																
1269	PG&E - Implementation Plan	31 days	Fri 11/11/22	Fri 12/23/22																
1270	PG&E - Local (C&S Compliance Improvement) Solicitation	436 days	Tue 3/1/22	Tue 10/31/23																
1271	PG&E - RFA Preparation	34 days	Tue 3/1/22	Fri 4/15/22																
1272	PG&E - RFA Release	1 day	Mon 5/16/22	Mon 5/16/22																
1273	PG&E - RFA Abstract Creation Duration	25 days	Tue 5/17/22	Mon 6/20/22																
1274	PG&E - RFA Evaluation	28 days	Tue 6/21/22	Thu 7/28/22																
1275	PG&E - RFA Review with EE PRG	1 day	Tue 8/9/22	Tue 8/9/22																
1276	PG&E - RFA Estimated Bidder Notification	1 day	Wed 8/31/22	Wed 8/31/22																
1277	PG&E - RFP Preparation	24 days	Mon 8/1/22	Thu 9/1/22																
1278	PG&E - RFP Release	1 day	Tue 9/13/22	Tue 9/13/22																
1279	PG&E - RFP Proposal Creation Duration	26 days	Tue 9/13/22	Tue 10/18/22																
1280	PG&E - RFP Evaluation	45 days	Wed 10/19/22	Tue 12/20/22																
1281	PG&E - RFP Review with EE PRG	1 day	Tue 1/24/23	Tue 1/24/23																
1282	PG&E - RFP Estimated Bidder Notification	1 day	Fri 2/10/23	Fri 2/10/23																
1283	PG&E - Contract Negotiation and Development	47 days	Mon 2/13/23	Tue 4/18/23																
1284	PG&E - Contract Review with EE PRG	26 days	Tue 5/23/23	Tue 6/27/23																
1285	PG&E - Final Award and Contract Signed	48 days	Wed 6/28/23	Fri 9/1/23																
1286	PG&E - Submit Advice Letter		N/A																	
1287	PG&E - Advice Letter Approved		N/A																	
1288	PG&E - Implementation Plan	1 day	Tue 10/31/23	Tue 10/31/23																
1289	PG&E - Residential Electrification Equity Program Solicitation	605 days	Mon 8/1/22	Fri 11/22/24																
1290	PG&E - RFA Preparation	59 days	Mon 8/1/22	Thu 10/20/22																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1291	PG&E - RFA Release	1 day	Tue 11/29/22	Tue 11/29/22																
1292	PG&E - RFA Abstract Creation Duration	46 days	Tue 11/29/22	Tue 1/31/23																
1293	PG&E - RFA Evaluation	17 days	Sun 2/5/23	Sun 2/26/23																
1294	PG&E - RFA Review with EE PRG	6 days	Mon 2/27/23	Mon 3/6/23																
1295	PG&E - RFA Estimated Bidder Notification	3 days	Mon 3/6/23	Wed 3/8/23																
1296	PG&E - RFP Preparation	46 days	Mon 1/9/23	Mon 3/13/23																
1297	PG&E - RFP Release	1 day	Tue 4/11/23	Tue 4/11/23																
1298	PG&E - RFP Proposal Creation Duration	26 days	Tue 4/11/23	Tue 5/16/23																
1299	PG&E - RFP Evaluation	18 days	Fri 5/19/23	Tue 6/13/23																
1300	PG&E - RFP Review with EE PRG	1 day	Tue 6/27/23	Tue 6/27/23																
1301	PG&E - RFP Estimated Bidder Notification	1 day	Tue 7/11/23	Tue 7/11/23																
1302	PG&E - Contract Negotiation and Development	233 days	Tue 8/1/23	Thu 6/20/24																
1303	PG&E - Contract Review with EE PRG	8 days	Fri 6/21/24	Tue 7/2/24																
1304	PG&E - Final Award and Contract Signed	21 days	Fri 7/5/24	Fri 8/2/24																
1305	PG&E - Submit Advice Letter	1 day	Fri 8/9/24	Fri 8/9/24																
1306	PG&E - Advice Letter Approved	1 day	Mon 9/23/24	Mon 9/23/24																
1307	PG&E - Implementation Plan	1 day	Fri 11/22/24	Fri 11/22/24																
1308	PG&E - Statewide C&S Advocacy Solicitation	641 days	Tue 2/1/22	Tue 7/16/24																
1309	PG&E - RFA Preparation	54 days	Tue 2/1/22	Fri 4/15/22																
1310	PG&E - RFA Release	1 day	Mon 5/30/22	Mon 5/30/22																
1311	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/31/22	Fri 7/1/22																
1312	PG&E - RFA Evaluation	14 days	Fri 7/1/22	Wed 7/20/22																
1313	PG&E - RFA Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22																
1314	PG&E - RFA Estimated Bidder Notification	1 day	Mon 8/1/22	Mon 8/1/22																
1315	PG&E - RFP Preparation	36 days	Fri 4/1/22	Fri 5/20/22																
1316	PG&E - RFP Release	1 day	Tue 6/7/22	Tue 6/7/22																
1317	PG&E - RFP Proposal Creation Duration	31 days	Tue 6/7/22	Tue 7/19/22																
1318	PG&E - RFP Evaluation	50 days	Wed 7/20/22	Tue 9/27/22																
1319	PG&E - RFP Review with EE PRG	1 day	Wed 10/5/22	Wed 10/5/22																
1320	PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/24/22	Mon 10/24/22																
1321	PG&E - Contract Negotiation and Development	73 days	Mon 11/14/22	Wed 2/22/23																
1322	PG&E - Contract Review with EE PRG - Wave 1	1 day	Tue 4/25/23	Tue 4/25/23																
1323	PG&E - Final Award and Contract Signed	18 days	Mon 7/17/23	Wed 8/9/23																
1324	PG&E - Submit Advice Letter (wave 1)	1 day	Thu 9/21/23	Thu 9/21/23																
1325	PG&E - Advice Letter Approved	1 day	Wed 10/25/23	Wed 10/25/23																
1326	PG&E - Implementation Plan	1 day	Thu 12/7/23	Thu 12/7/23																
1327	PG&E - Contract Review with EE PRG - Wave 2	1 day	Wed 12/20/23	Wed 12/20/23																
1328	PG&E - Final Award and Contract Signed	1 day	Fri 3/29/24	Fri 3/29/24																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1329	PG&E - Submit Advice Letter	1 day	Wed 4/17/24	Wed 4/17/24																
1330	PG&E - Advice Letter Approved	1 day	Fri 5/17/24	Fri 5/17/24																
1331	PG&E - Implementation Plan	1 day	Tue 7/16/24	Tue 7/16/24																
1332	PG&E - Zonal Electrification Solicitation	495 days	Thu 12/1/22	Wed 10/23/24																
1333	PG&E - RFP Preparation	88 days	Thu 12/1/22	Mon 4/3/23																
1334	PG&E - RFP Release	1 day	Tue 4/18/23	Tue 4/18/23																
1335	PG&E - RFP Proposal Creation Duration	53 days	Tue 4/18/23	Thu 6/29/23																
1336	PG&E - RFP Evaluation (including interviews)	40 days	Mon 7/10/23	Fri 9/1/23																
1337	PG&E - RFP Review with EE PRG	1 day	Tue 9/26/23	Tue 9/26/23																
1338	PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/2/23	Mon 10/2/23																
1339	PG&E - Contract Negotiation and Development	135 days	Mon 10/9/23	Fri 4/12/24																
1340	PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24																
1341	PG&E - Final Award and Contract Signed	43 days	Wed 5/1/24	Fri 6/28/24																
1342	PG&E - Submit Advice Letter	1 day	Wed 7/3/24	Wed 7/3/24																
1343	PG&E - Advice Letter Approved	1 day	Wed 8/28/24	Wed 8/28/24																
1344	PG&E - Implementation Plan	1 day	Wed 10/23/24	Wed 10/23/24																
1345	PG&E - Residential Whole Home Load Management RFP	453 days	Tue 8/15/23	Thu 5/8/25																
1346	PG&E - RFP Preparation	1 day	Tue 8/15/23	Tue 8/15/23																
1347	PG&E - RFP Release	1 day	Tue 8/15/23	Tue 8/15/23																
1348	PG&E - RFP Proposal Creation Duration	51 days	Tue 8/15/23	Tue 10/24/23																
1349	PG&E - RFP Evaluation	36 days	Thu 10/26/23	Thu 12/14/23																
1350	PG&E - RFP Review with EE PRG	1 day	Fri 2/16/24	Fri 2/16/24																
1351	PG&E - RFP Estimated Bidder Notification	1 day	Tue 2/27/24	Tue 2/27/24																
1352	PG&E - Contract Negotiation and Development	155 days	Wed 3/13/24	Tue 10/15/24																
1353	PG&E - Contract Review with EE PRG	11 days	Wed 10/16/24	Wed 10/30/24																
1354	PG&E - Final Award and Contract Signed	50 days	Wed 11/6/24	Tue 1/14/25																
1355	PG&E - Submit Advice Letter	1 day	Thu 1/23/25	Thu 1/23/25																
1356	PG&E - Advice Letter Approved	1 day	Sun 3/9/25	Sun 3/9/25																
1357	PG&E - Implementation Plan	1 day	Thu 5/8/25	Thu 5/8/25																
1358	PG&E - 2024 Summer Reliability Platform Administrator RFP	337 days?	Tue 4/18/23	Wed 7/31/24																
1359	PG&E - RFP Preparation	30 days	Mon 5/1/23	Fri 6/9/23																
1360	PG&E - RFP Release	1 day	Fri 9/1/23	Fri 9/1/23																
1361	PG&E - RFP Proposal Creation Duration	31 days	Fri 9/1/23	Fri 10/13/23																
1362	PG&E - RFP Evaluation	22 days	Tue 10/17/23	Wed 11/15/23																
1363	PG&E - RFP Review with EE PRG	1 day	Tue 11/28/23	Tue 11/28/23																
1364	PG&E - RFP Estimated Bidder Notification	1 day	Tue 12/5/23	Tue 12/5/23																
1365	PG&E - Contract Negotiation and Development	68 days	Mon 1/8/24	Wed 4/10/24																
1366	PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1367	PG&E - Final Award and Contract Signed	22 days	Wed 5/1/24	Thu 5/30/24																
1368	PG&E - Submit Advice Letter	1 day	Fri 5/31/24	Fri 5/31/24																
1369	PG&E - Advice Letter Approved	1 day	Mon 7/1/24	Mon 7/1/24																
1370	PG&E - Implementation Plan	1 day	Wed 7/31/24	Wed 7/31/24																
1371	PG&E - C&S Code Readiness RFP	393 days?	Wed 2/1/23	Fri 8/2/24																
1372	PG&E - RFP Preparation	113 days	Wed 2/1/23	Fri 7/7/23																
1373	PG&E - RFP Release	1 day	Wed 7/12/23	Wed 7/12/23																
1374	PG&E - RFP Proposal Creation Duration	30 days	Thu 7/13/23	Wed 8/23/23																
1375	PG&E - RFP Evaluation	36 days	Mon 8/28/23	Mon 10/16/23																
1376	PG&E - RFP Review with EE PRG	1 day	Tue 10/24/23	Tue 10/24/23																
1377	PG&E - RFP Estimated Bidder Notification	1 day	Mon 11/6/23	Mon 11/6/23																
1378	PG&E - Contract Negotiation and Development	65 days	Wed 11/15/23	Tue 2/13/24																
1379	PG&E - Contract Review with EE PRG	1 day	Tue 2/27/24	Tue 2/27/24																
1380	PG&E - Final Award and Contract Signed	1 day	Fri 4/12/24	Fri 4/12/24																
1381	PG&E - Submit Advice Letter	1 day	Tue 5/7/24	Tue 5/7/24																
1382	PG&E - Advice Letter Approved	1 day	Thu 6/6/24	Thu 6/6/24																
1383	PG&E - Implementation Plan	1 day	Fri 8/2/24	Fri 8/2/24																
1384	PG&E - Residential Electrification - Single Point of Contact	414 days	Tue 8/1/23	Fri 2/28/25																
1385	PG&E - RFP Preparation	133 days	Tue 8/1/23	Thu 2/1/24																
1386	PG&E - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24																
1387	PG&E - RFP Proposal Creation Duration	33 days	Wed 2/28/24	Fri 4/12/24																
1388	PG&E - RFP Evaluation	66 days	Mon 4/15/24	Mon 7/15/24																
1389	PG&E - RFP Review with EE PRG	6 days	Fri 7/19/24	Fri 7/26/24																
1390	PG&E - RFP Estimated Bidder Notification	1 day	Wed 8/7/24	Wed 8/7/24																
1391	PG&E - Contract Negotiation and Development	62 days																		
1392	PG&E - Contract Review with EE PRG	6 days																		
1393	PG&E - Final Award and Contract Signed	25 days																		
1394	PG&E - Submit Advice Letter	1 day																		
1395	PG&E - Advice Letter Approved	1 day																		
1396	PG&E - Implementation Plan	1 day																		
1397	PG&E - Commercial SEM FP	428 days?	Thu 8/3/23	Mon 3/24/25																
1398	PG&E - RFP Preparation	16 days	Thu 8/3/23	Thu 8/24/23																
1399	PG&E - RFP Release	1 day	Fri 11/3/23	Fri 11/3/23																
1400	PG&E - RFP Proposal Creation Duration	55 days	Fri 11/3/23	Thu 1/18/24																
1401	PG&E - RFP Evaluation	58 days	Tue 1/23/24	Thu 4/11/24																
1402	PG&E - RFP Review with EE PRG	1 day	Wed 4/17/24	Wed 4/17/24																
1403	PG&E - RFP Estimated Bidder Notification	4 days	Tue 4/23/24	Fri 4/26/24																
1404	PG&E - Contract Negotiation and Development	90 days	Thu 5/2/24	Wed 9/4/24																

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025	
					H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2		
1405	PG&E - Contract Review with EE PRG	6 days	Fri 9/13/24	Fri 9/20/24																
1406	PG&E - Final Award and Contract Signed	51 days	Wed 9/25/24	Wed 12/4/24																
1407	PG&E - Submit Advice Letter	1 day	Mon 12/9/24	Mon 12/9/24																
1408	PG&E - Advice Letter Approved	1 day	Thu 1/23/25	Thu 1/23/25																
1409	PG&E - Implementation Plan	1 day	Mon 3/24/25	Mon 3/24/25																
1410																				
1411																				

Project: IOU Master Task Timeli
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
